US Army Corps of Engineers ®

P2 – RMS Interface

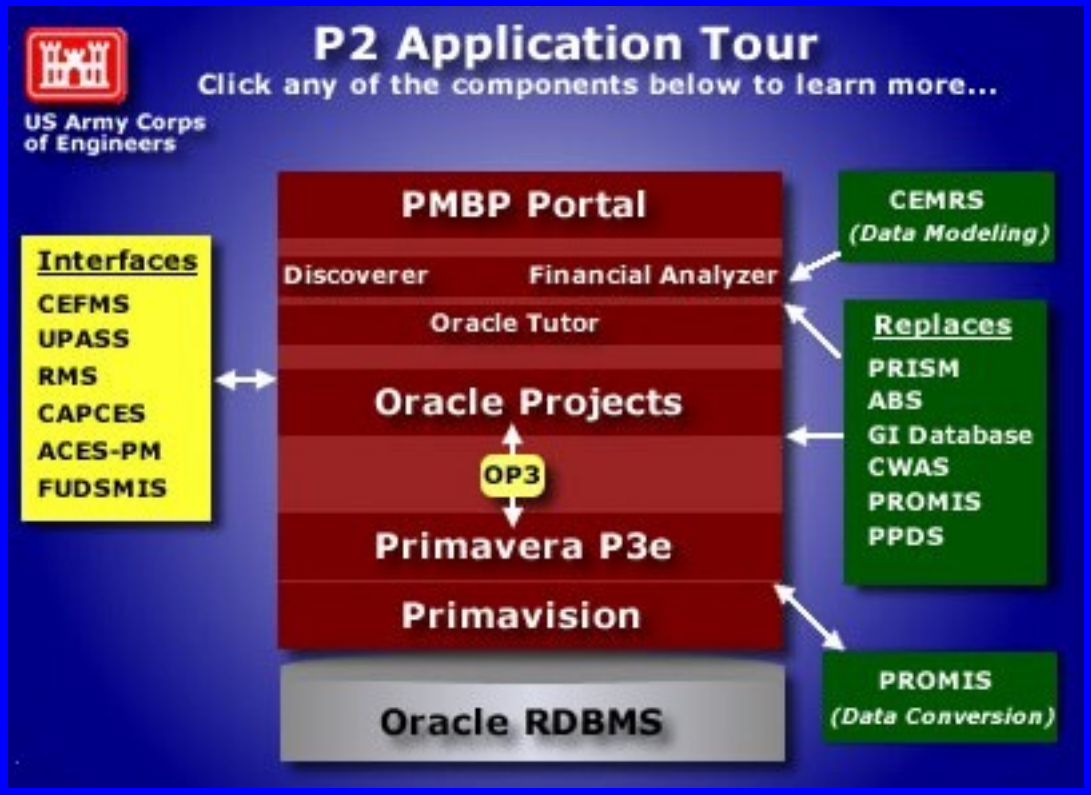

May 2010

US Army Corps of Engineers ®

P2 – RMS Interface

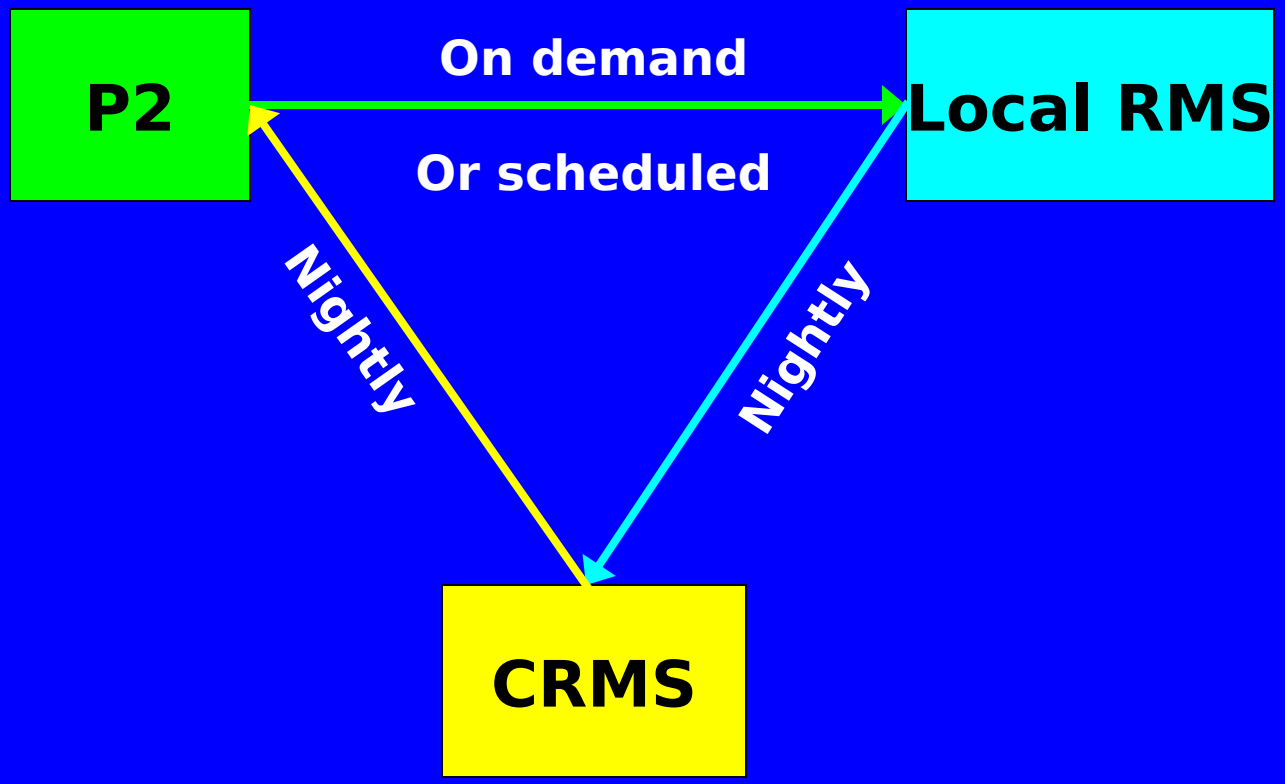

US Army Corps of Engineers ®

P2 – RMS Interface

- One P2 Project to one RMS Contract
- One P2 Project to multiple RMS Contracts
- Multiple P2 Projects to one RMS Contract

US Army Corps of Engineers ®

P2 – RMS Interface

- Schedule Dates
  - P2 controls prior to Contract Award
  - RMS controls after Contract Award
- P2 controls budget
- CEFMS controls funds

RMS download from P2

- Project Information
  - Project ID
  - Project Title
  - WBS
  - WBS Title
  - Task Code
  - Task Name
  - Task Amount
  - Design By
  - Contract Type
  - Project – Scope of Work
  - Contract Status Code
  - Primary Delay Code
  - Project – Customer Issues
  - Project – USACE Issues
  - Task Organization (P2 Org Code)
- Milestone Dates (Target Dates)
  - Contract Award Date
  - NTP Acknowledged Date
  - Contract Required Completion Date
  - Construction Completion Date
  - Beneficial Occupancy Date
  - Physical Completion Date
  - Transfer Document Date
  - AE Evaluation Date
  - Contractor Evaluation Date
  - Contractor Final Payment Date

US Army Corps of Engineers

CRMS download to P2

- Contract Information
  - Contract Number
  - Delivery Order Number
  - Contract Title
  - Contract Scope of Work
  - Contract Amount
  - Placement Percentage
  - Contract Status Code
  - Primary Delay Code
  - Phase (WBS) Title
  - Contract – Customer Issues
  - Contract – USACE Issues
  - Phase Title on Multiphase Contracts
- Milestone Dates
  - Contract Award Date
  - NTP Acknowledged Date
  - Contract Required Completion Date
  - Construction Completion Date
  - Beneficial Occupancy Date
  - Physical Completion Date
  - Transfer Document Date
  - AE Evaluation Date
  - Contractor Evaluation Date
  - Contractor Final Payment Date

US Army Corps of Engineers ®

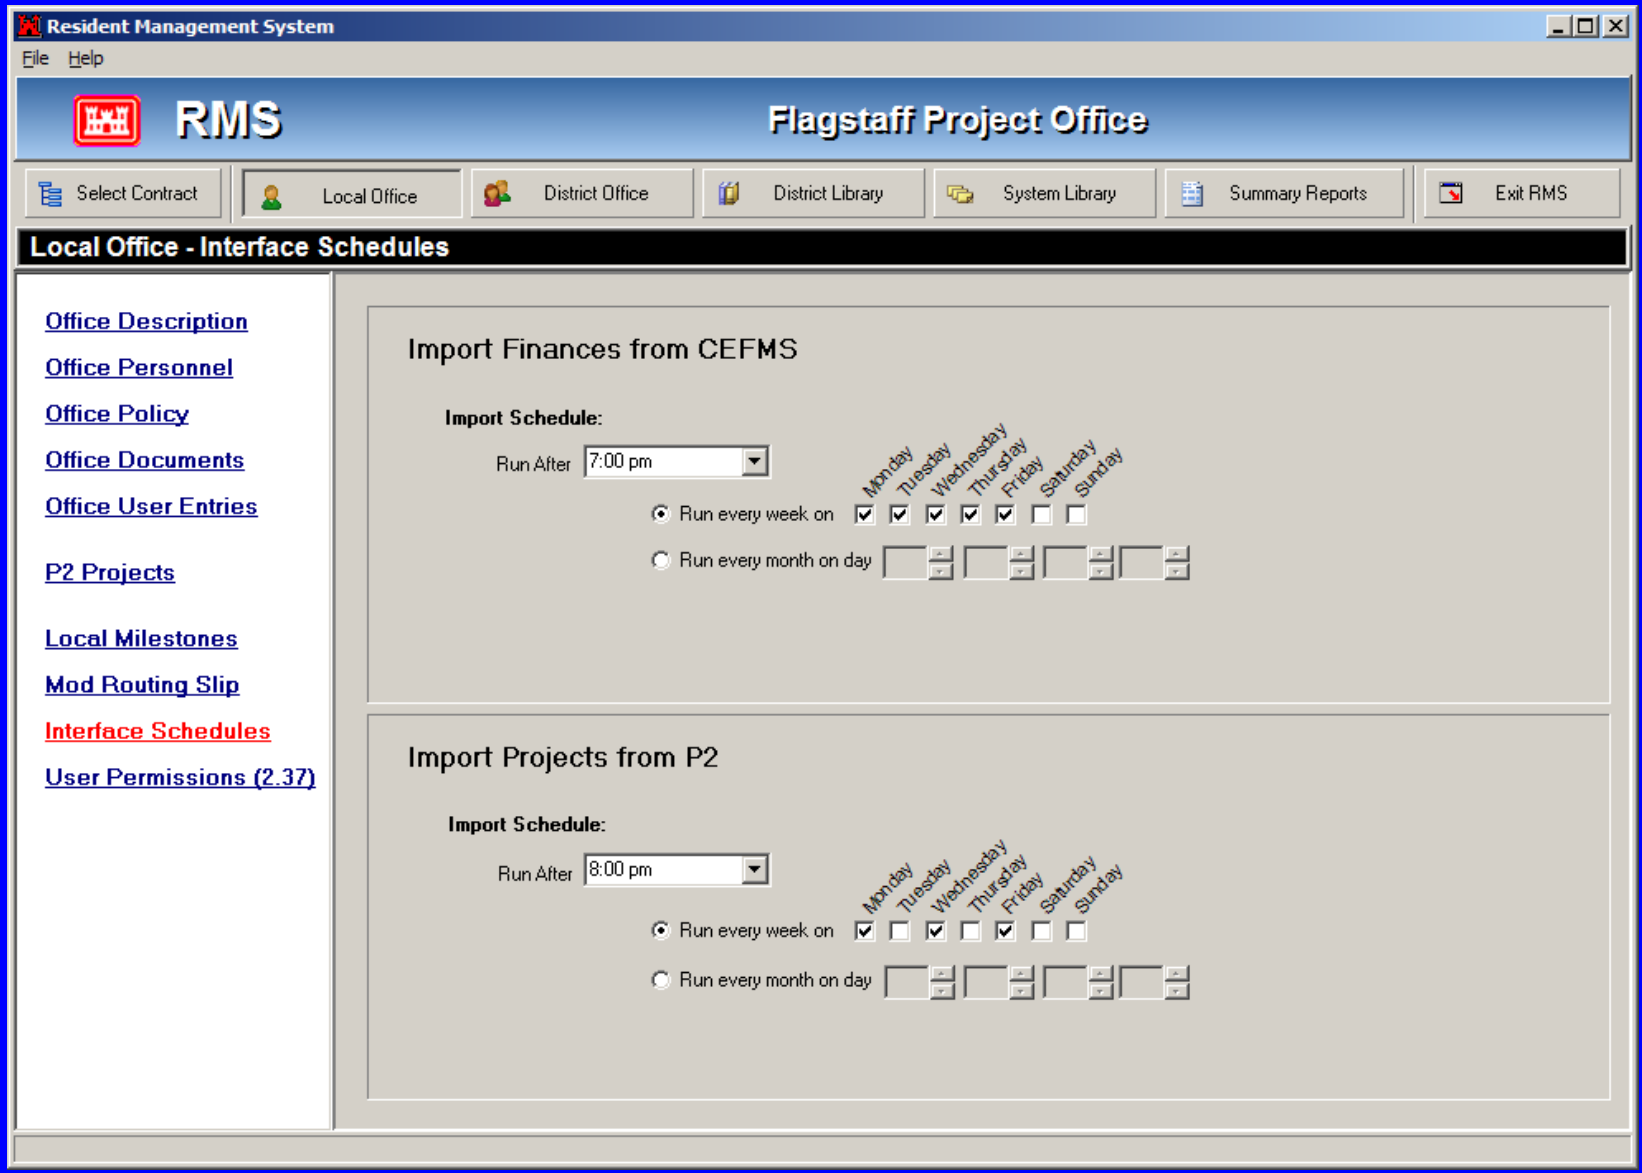

P2 Project ID and Project Title

WBS No. and WBS Title

Task Code / Activity ID

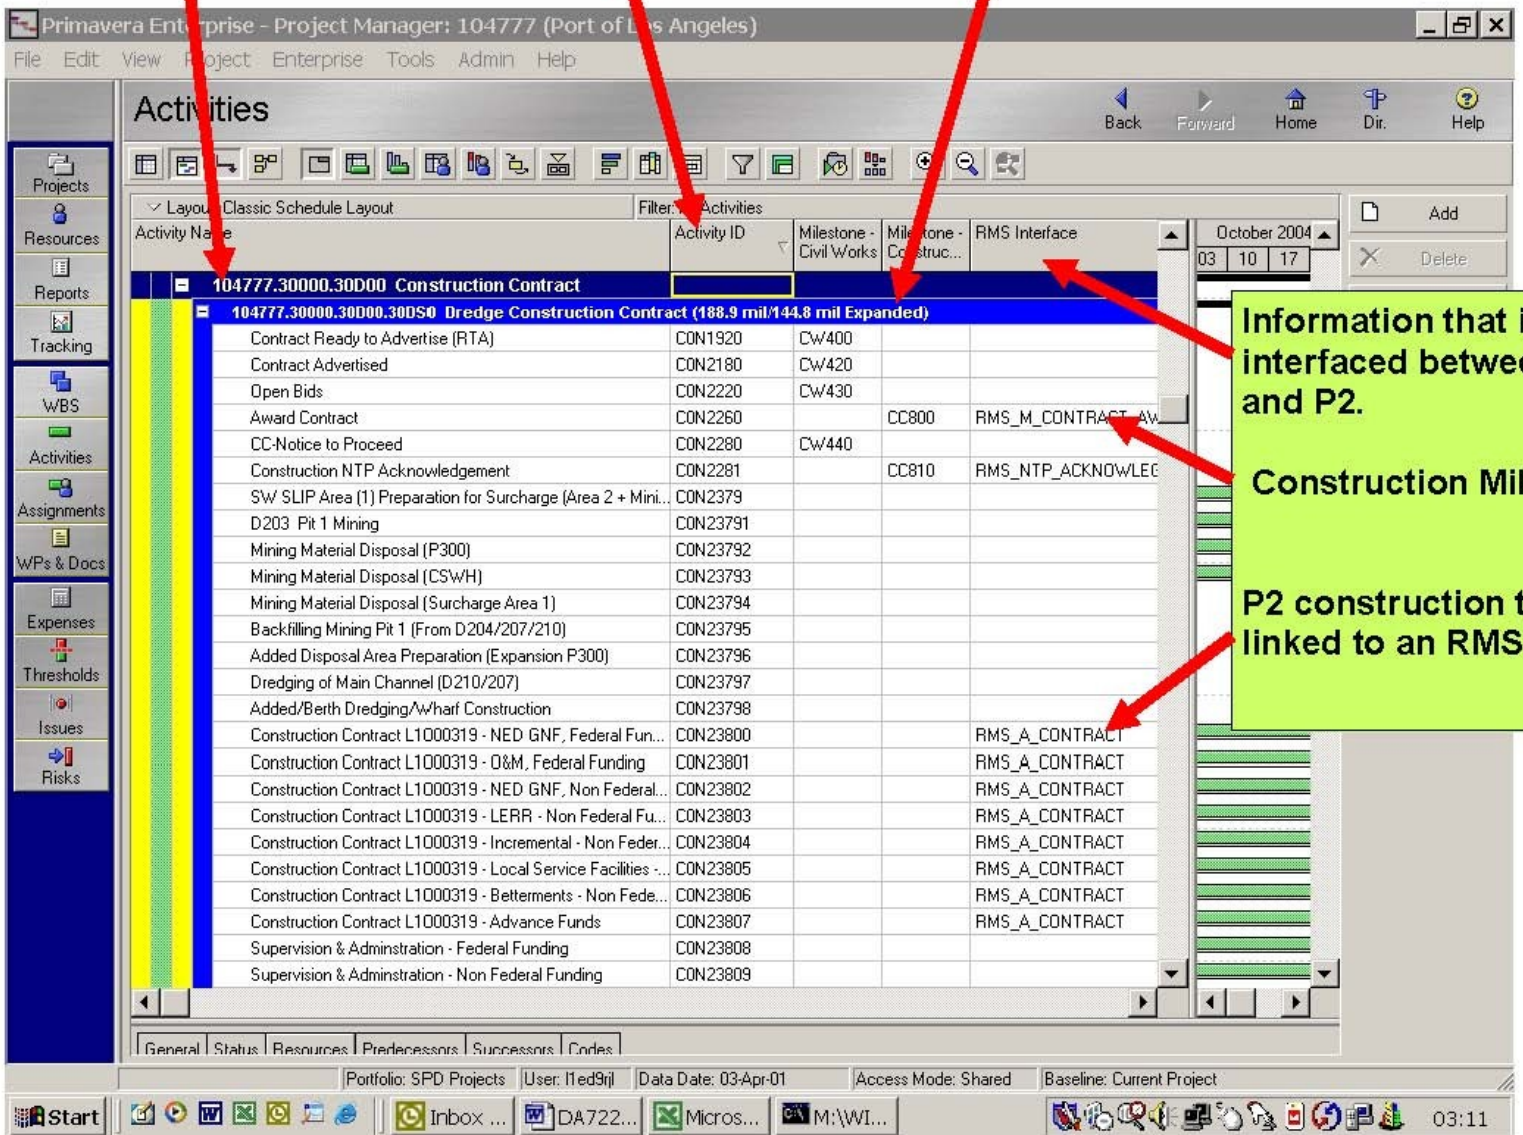
Primavera Enterprise - Project Manager: 104777 (Port of Los Angeles)
File Edit View Project Enterprise Tools Admin Help
Activities
Back Forward Home Dir. Help
Projects Resources Reports Tracking WBS Activities Assignments WPs & Docs Expenses Thresholds Issues Risks
Layout: Classic Schedule Layout
Filter: Activities
Activity Name
Activity ID
Milestone - Civil Works
Milestone - Construc...
RMS Interface
October 2004
03 10 17
Add
Delete
104777.30000.30D00 Construction Contract
104777.30000.30D00.30DS0 Dredge Construction Contract (188.9 mil/144.8 mil Expanded)
Contract Ready to Advertise (RTA) CON1920 CW400
Contract Advertised CON2180 CW420
Open Bids CON2220 CW430
Award Contract CON2260 CC800 RMS_M_CONTRACT_AW
CC-Notice to Proceed CON2280 CW440
Construction NTP Acknowledgement CON2281 CC810 RMS_NTP_ACKNOWLEG
SW SLIP Area (1) Preparation for Surcharge (Area 2 + Mini... CON2379
D203 Pit 1 Mining CON23791
Mining Material Disposal (P300) CON23792
Mining Material Disposal (CSWH) CON23793
Mining Material Disposal (Surcharge Area 1) CON23794
Backfilling Mining Pit 1 (From D204/207/210) CON23795
Added Disposal Area Preparation (Expansion P300) CON23796
Dredging of Main Channel (D210/207) CON23797
Added/Berth Dredging/Wharf Construction CON23798
Construction Contract L1000319 - NED GNF, Federal Fun... CON23800 RMS_A_CONTRACT
Construction Contract L1000319 - O&M, Federal Funding CON23801 RMS_A_CONTRACT
Construction Contract L1000319 - NED GNF, Non Federal... CON23802 RMS_A_CONTRACT
Construction Contract L1000319 - LERR - Non Federal Fu... CON23803 RMS_A_CONTRACT
Construction Contract L1000319 - Incremental - Non Feder... CON23804 RMS_A_CONTRACT
Construction Contract L1000319 - Local Service Facilities -... CON23805 RMS_A_CONTRACT
Construction Contract L1000319 - Betterments - Non Fede... CON23806 RMS_A_CONTRACT
Construction Contract L1000319 - Advance Funds CON23807 RMS_A_CONTRACT
Supervision & Adminstration - Federal Funding CON23808
Supervision & Adminstration - Non Federal Funding CON23809
General Status Resources Predecessors Successors Codes
Portfolio: SPD Projects User: l1ed9rjl Data Date: 03-Apr-01 Access Mode: Shared Baseline: Current Project
Start Inbox ... DA722... Micros... M:\WI... 03:11

Information that is interfaced between RMS and P2.

Construction Milestones

P2 construction tasks linked to an RMS Contract

US Army Corps of Engineers ®

P2 Project Number and Title

Milestone Dates

WBS/Activity Costs

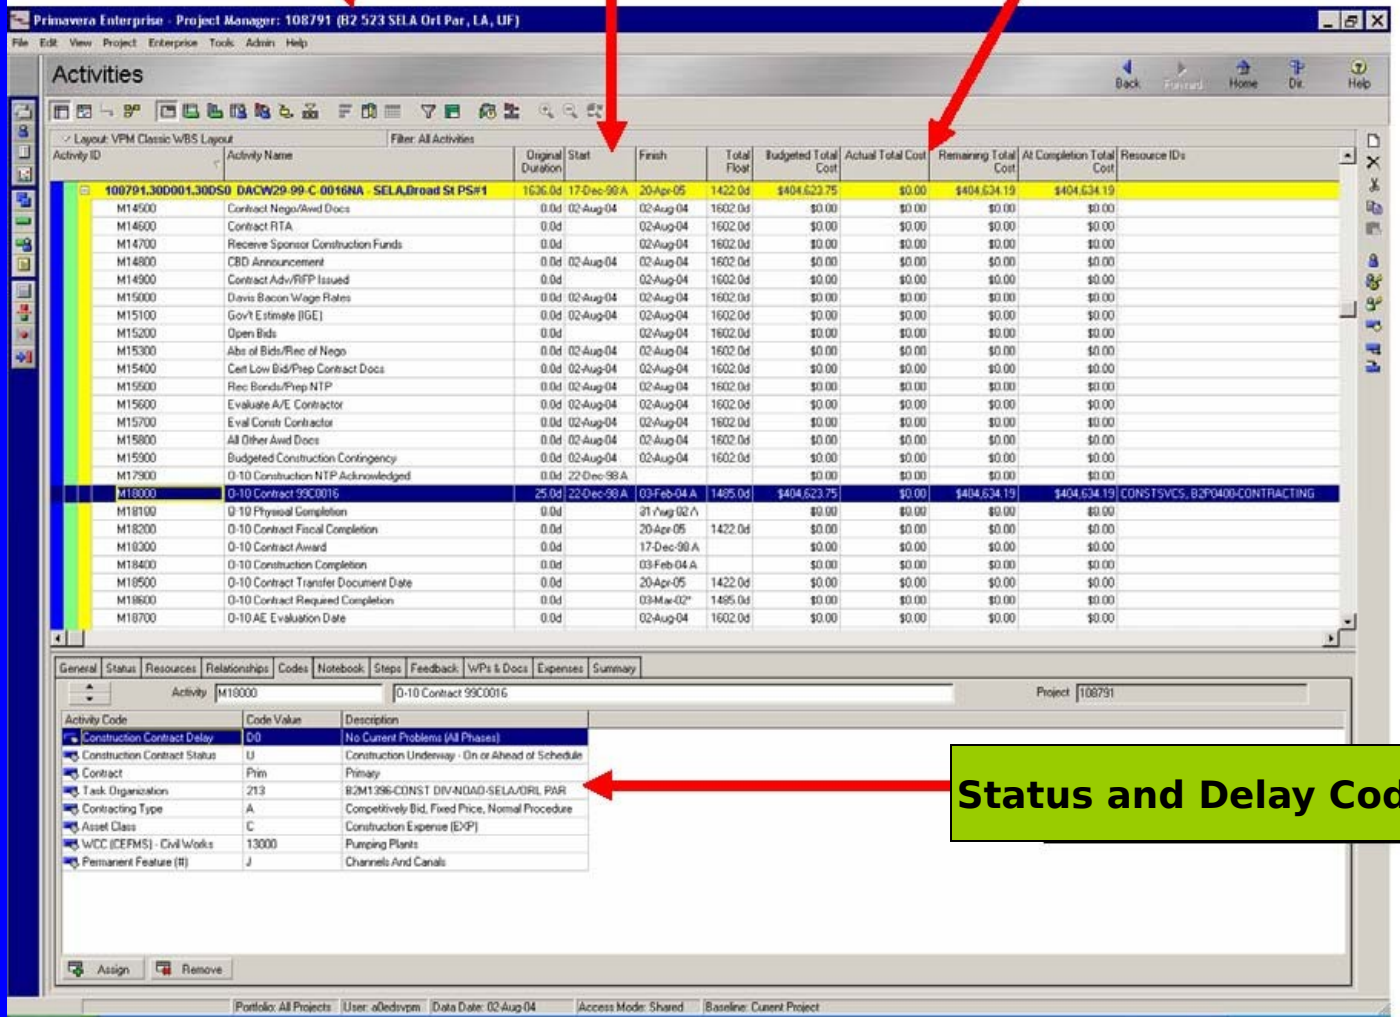
Primavera Enterprise - Project Manager: 108791 (B2 523 SELA Orl Par, LA, UF)
File Edit View Project Enterprise Tools Admin Help
Activities
Back Forward Home Dir. Help
Layout: VPM Classic WBS Layout
Filter: All Activities
Activity ID
Activity Name
Original Duration
Start
Finish
Total Float
Budgeted Total Cost
Actual Total Cost
Remaining Total Cost
At Completion Total Cost
Resource IDs
100791.30D001.30DS0 DACW29-99-C 0016NA - SELA,Broad St PS#1 1636.0d 17-Dec-98 A 20-Apr-05 1422.0d $404,623.75 $0.00 $404,634.19 $404,634.19
M14500 Contract Nego/Awd Docs 0.0d 02-Aug-04 02-Aug-04 1602.0d $0.00 $0.00 $0.00 $0.00
M14600 Contract RTA 0.0d 02-Aug-04 1602.0d $0.00 $0.00 $0.00 $0.00
M14700 Receive Sponsor Construction Funds 0.0d 02-Aug-04 1602.0d $0.00 $0.00 $0.00 $0.00
M14800 CBD Announcement 0.0d 02-Aug-04 02-Aug-04 1602.0d $0.00 $0.00 $0.00 $0.00
M14900 Contract Adv/RFP Issued 0.0d 02-Aug-04 1602.0d $0.00 $0.00 $0.00 $0.00
M15000 Davis Bacon Wage Rates 0.0d 02-Aug-04 02-Aug-04 1602.0d $0.00 $0.00 $0.00 $0.00
M15100 Gov't Estimate (IGE) 0.0d 02-Aug-04 02-Aug-04 1602.0d $0.00 $0.00 $0.00 $0.00
M15200 Open Bids 0.0d 02-Aug-04 1602.0d $0.00 $0.00 $0.00 $0.00
M15300 Abs of Bids/Rec of Nego 0.0d 02-Aug-04 02-Aug-04 1602.0d $0.00 $0.00 $0.00 $0.00
M15400 Cert Low Bid/Prep Contract Docs 0.0d 02-Aug-04 02-Aug-04 1602.0d $0.00 $0.00 $0.00 $0.00
M15500 Rec Bonds/Prep NTP 0.0d 02-Aug-04 02-Aug-04 1602.0d $0.00 $0.00 $0.00 $0.00
M15600 Evaluate A/E Contractor 0.0d 02-Aug-04 02-Aug-04 1602.0d $0.00 $0.00 $0.00 $0.00
M15700 Eval Constr Contractor 0.0d 02-Aug-04 02-Aug-04 1602.0d $0.00 $0.00 $0.00 $0.00
M15800 All Other Awd Docs 0.0d 02-Aug-04 02-Aug-04 1602.0d $0.00 $0.00 $0.00 $0.00
M15900 Budgeted Construction Contingency 0.0d 02-Aug-04 02-Aug-04 1602.0d $0.00 $0.00 $0.00 $0.00
M17900 0-10 Construction NTP Acknowledged 0.0d 22-Dec-98 A $0.00 $0.00 $0.00 $0.00
M18000 0-10 Contract 99C0016 25.0d 22-Dec-98 A 03-Feb-04 A 1485.0d $404,623.75 $0.00 $404,634.19 $404,634.19 CONSTSVCS, B2P0400-CONTRACTING
M18100 0-10 Physical Completion 0.0d 31-Aug-02 A $0.00 $0.00 $0.00 $0.00
M18200 0-10 Contract Fiscal Completion 0.0d 20-Apr-05 1422.0d $0.00 $0.00 $0.00 $0.00
M18300 0-10 Contract Award 0.0d 17-Dec-98 A $0.00 $0.00 $0.00 $0.00
M18400 0-10 Construction Completion 0.0d 03-Feb-04 A $0.00 $0.00 $0.00 $0.00
M18500 0-10 Contract Transfer Document Date 0.0d 20-Apr-05 1422.0d $0.00 $0.00 $0.00 $0.00
M18600 0-10 Contract Required Completion 0.0d 03-Mar-02* 1485.0d $0.00 $0.00 $0.00 $0.00
M18700 0-10 AE Evaluation Date 0.0d 02-Aug-04 1602.0d $0.00 $0.00 $0.00 $0.00
General Status Resources Relationships Codes Notebook Steps Feedback WPs & Docs Expenses Summary
Activity M18000 0-10 Contract 99C0016 Project 108791
Activity Code
Code Value
Description
Construction Contract Delay D0 No Current Problems (All Phases)
Construction Contract Status U Construction Underway - On or Ahead of Schedule
Contract Prim Primary
Task Organization 213 B2M1296-CONST DIV-NOAD-SELA/ORL PAR
Contracting Type A Competitively Bid, Fixed Price, Normal Procedure
Asset Class C Construction Expense (EXP)
WCC (CEFMS) - Civil Works 13000 Pumping Plants
Permanent Feature (H) J Channels And Canals
Assign Remove
Portfolio: All Projects User: aDedovpm Data Date: 02-Aug-04 Access Mode: Shared Baseline: Current Project

Status and Delay Codes

US Army Corps of Engineers ®

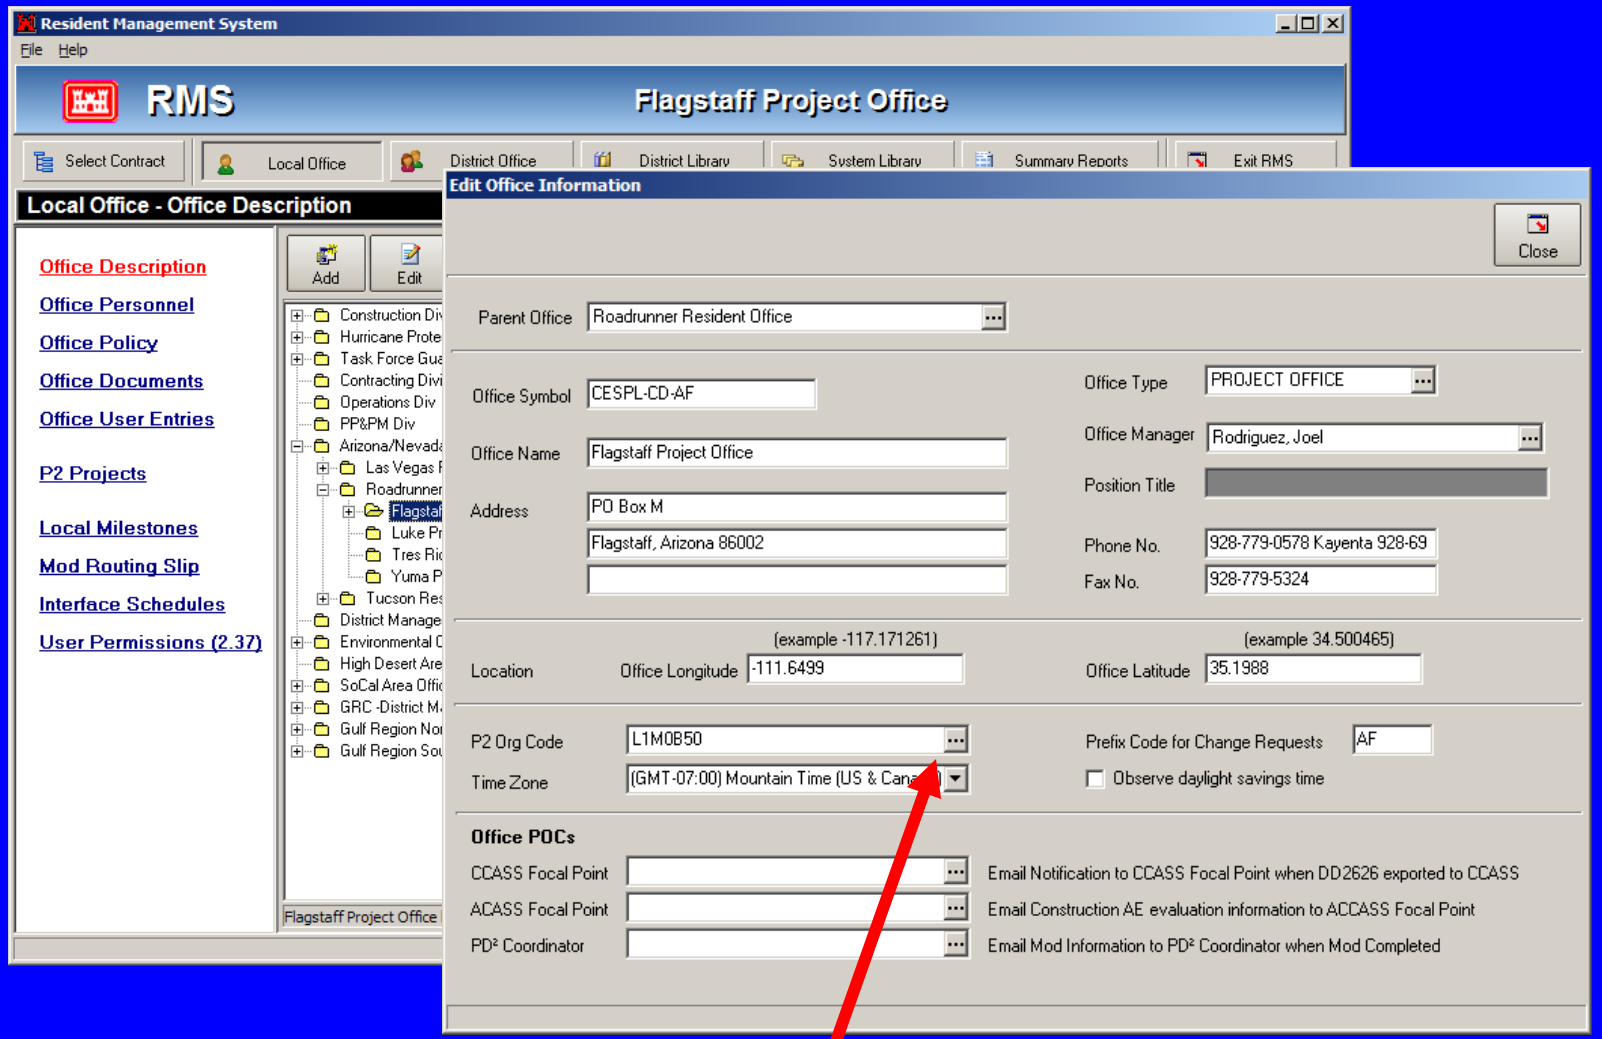

You can download the P2 Task Organizations by using the looku

US Army Corps of Engineers ®

Download P2 Data

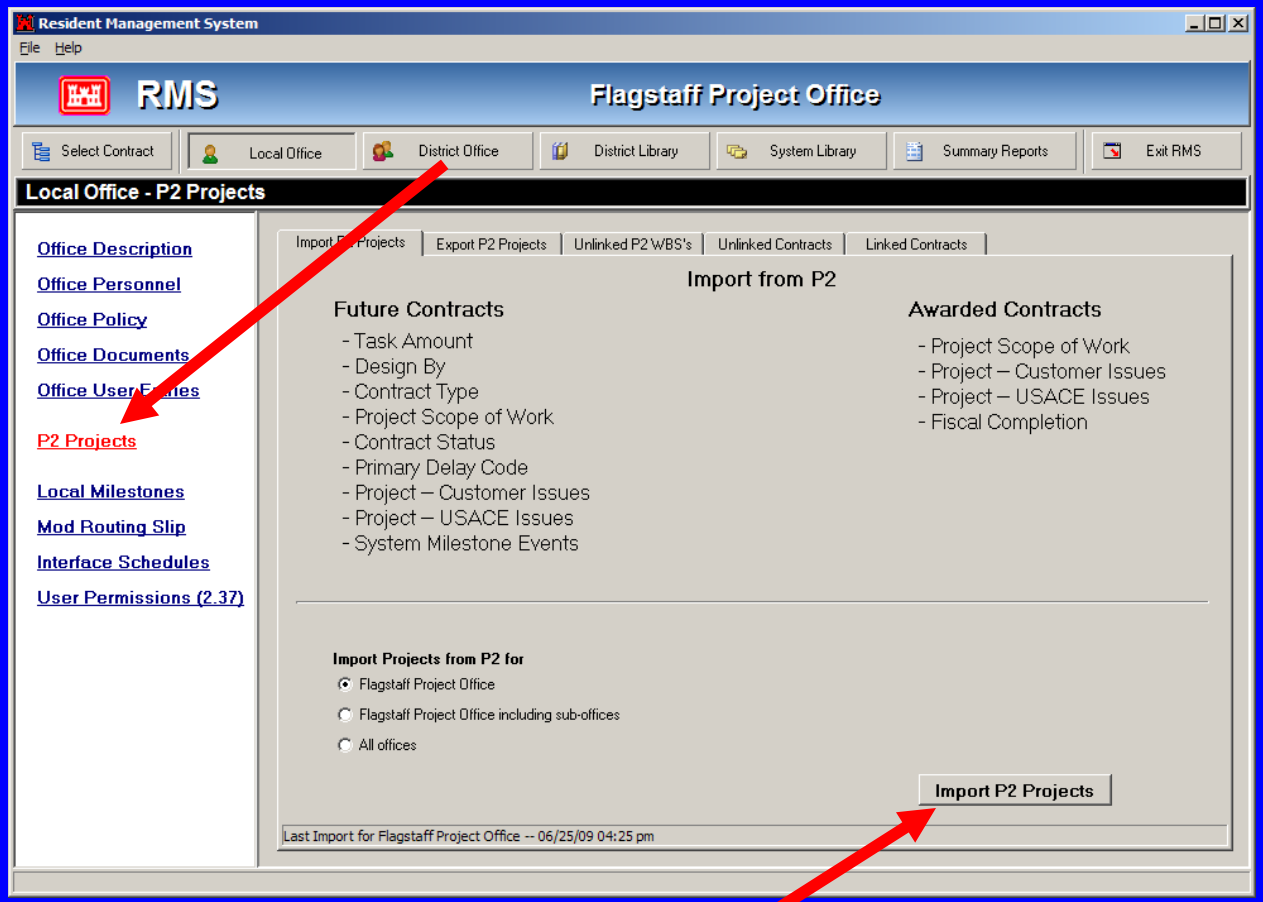

Once you have entered the P2 Task Organization Code for a particular office, you are ready to download the available P2 projects for that office. Click on the Home button, select the office you want to download P2 projects for, and then click the Summary button. The program will display the option P2 Projects and you should select that option.

US Army Corps of Engineers ®

Unlinked P2 WBS's

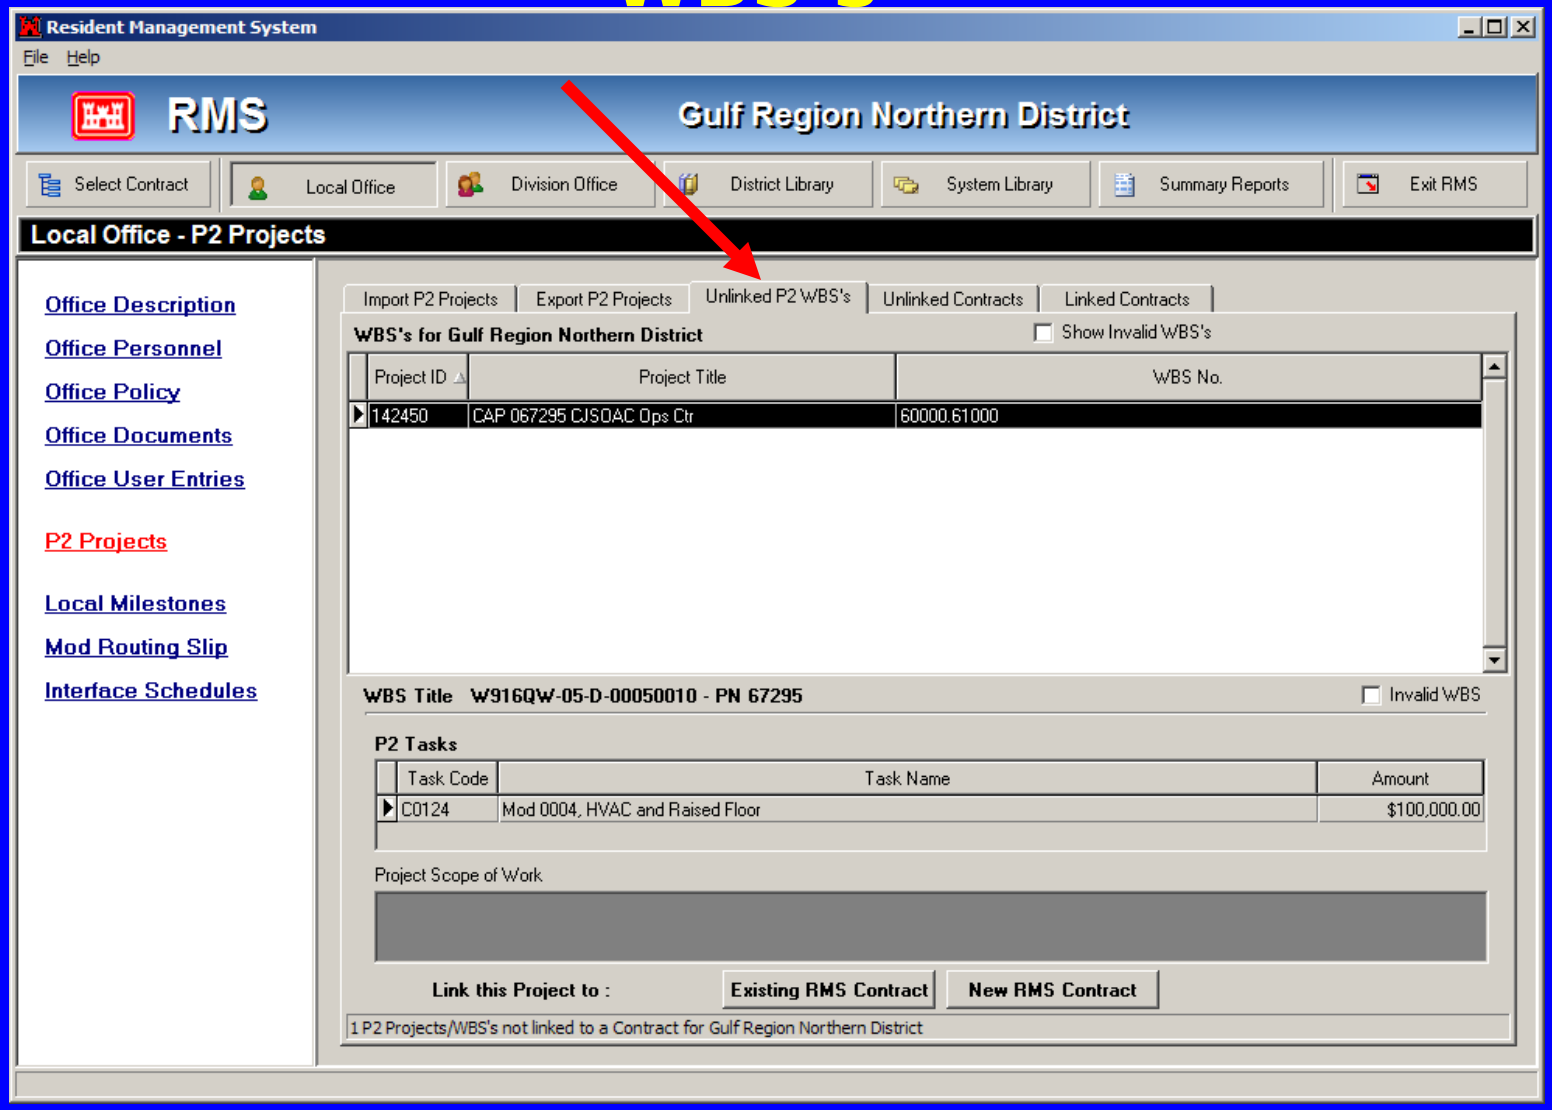

US Army Corps of Engineers ®

Identify and Link P2 Projects to RMS Contracts

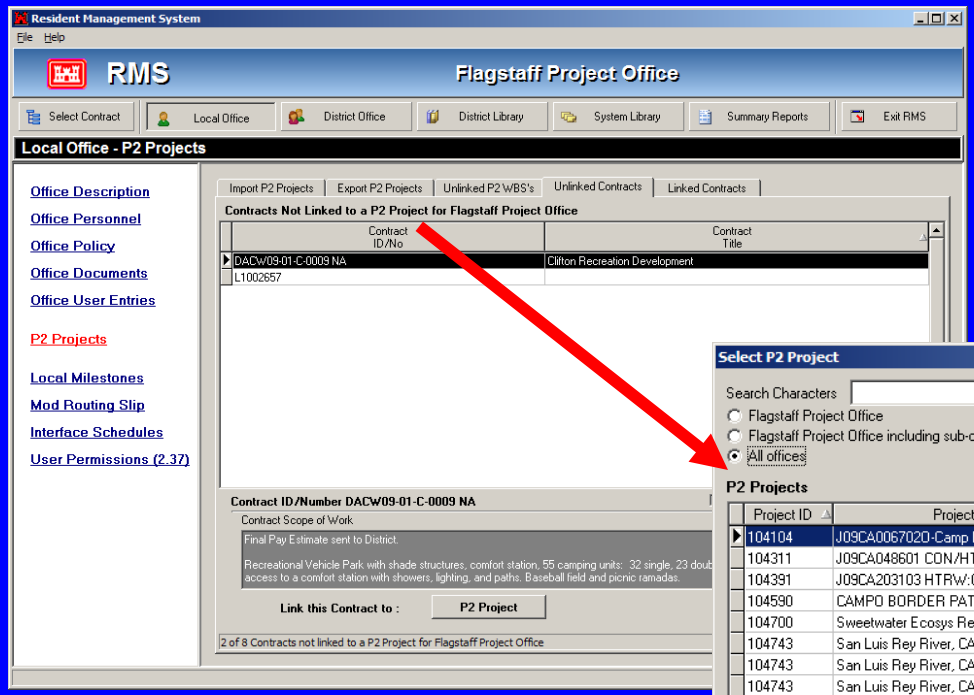

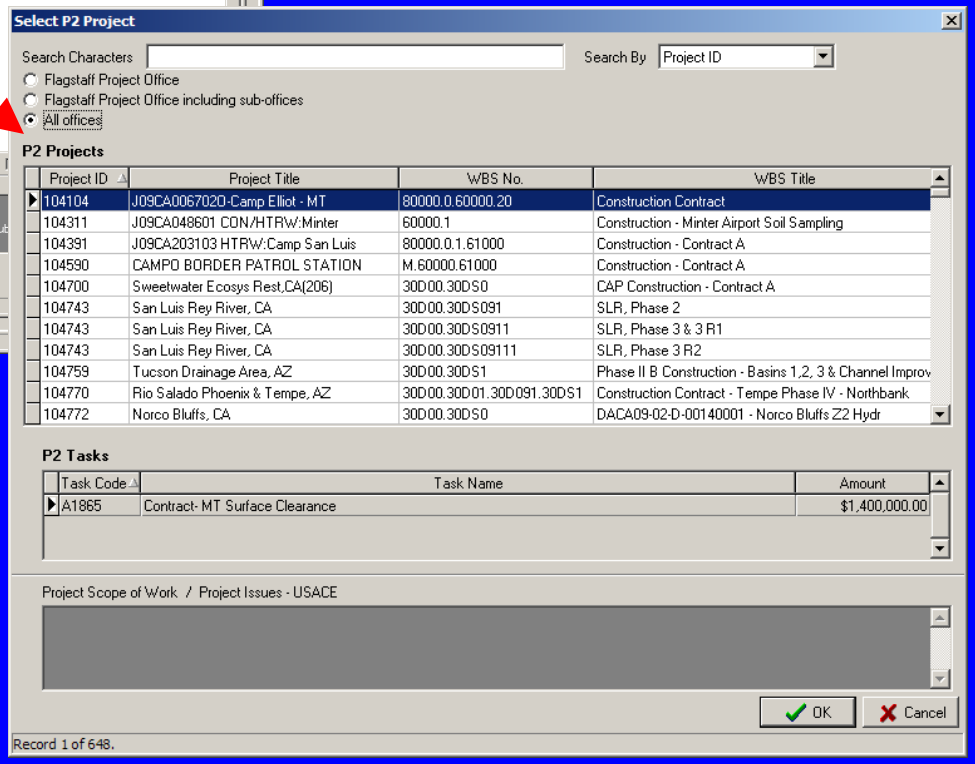
Select P2 Project
Search Characters
Search By
Project ID
Flagstaff Project Office
Flagstaff Project Office including sub-offices
All offices
P2 Projects
Project ID
Project Title
WBS No.
WBS Title
104104 J09CA0067020-Camp Elliot - MT 80000.0.60000.20 Construction Contract
104311 J09CA048601 CON/HTRW:Minter 60000.1 Construction - Minter Airport Soil Sampling
104391 J09CA203103 HTRW:Camp San Luis 80000.0.1.61000 Construction - Contract A
104590 CAMPO BORDER PATROL STATION M.60000.61000 Construction - Contract A
104700 Sweetwater Ecosys Rest,CA(206) 30D00.30DS0 CAP Construction - Contract A
104743 San Luis Rey River, CA 30D00.30DS091 SLR, Phase 2
104743 San Luis Rey River, CA 30D00.30DS0911 SLR, Phase 3 & 3 R1
104743 San Luis Rey River, CA 30D00.30DS09111 SLR, Phase 3 R2
104759 Tucson Drainage Area, AZ 30D00.30DS1 Phase II B Construction - Basins 1,2, 3 & Channel Improv
104770 Rio Salado Phoenix & Tempe, AZ 30D00.30D01.30D091.30DS1 Construction Contract - Tempe Phase IV - Northbank
104772 Norco Bluffs, CA 30D00.30DS0 DACA09-02-D-00140001 - Norco Bluffs Z2 Hydr
P2 Tasks
Task Code
Task Name
Amount
A1865 Contract- MT Surface Clearance $1,400,000.00
Project Scope of Work / Project Issues - USACE
OK
Cancel
Record 1 of 648.

Another area where you can link a P2 Project to an RMS contract is on the Contract Administration screen.

Controlling the RMS – P2 Interface

US Army Corps of Engineers ®

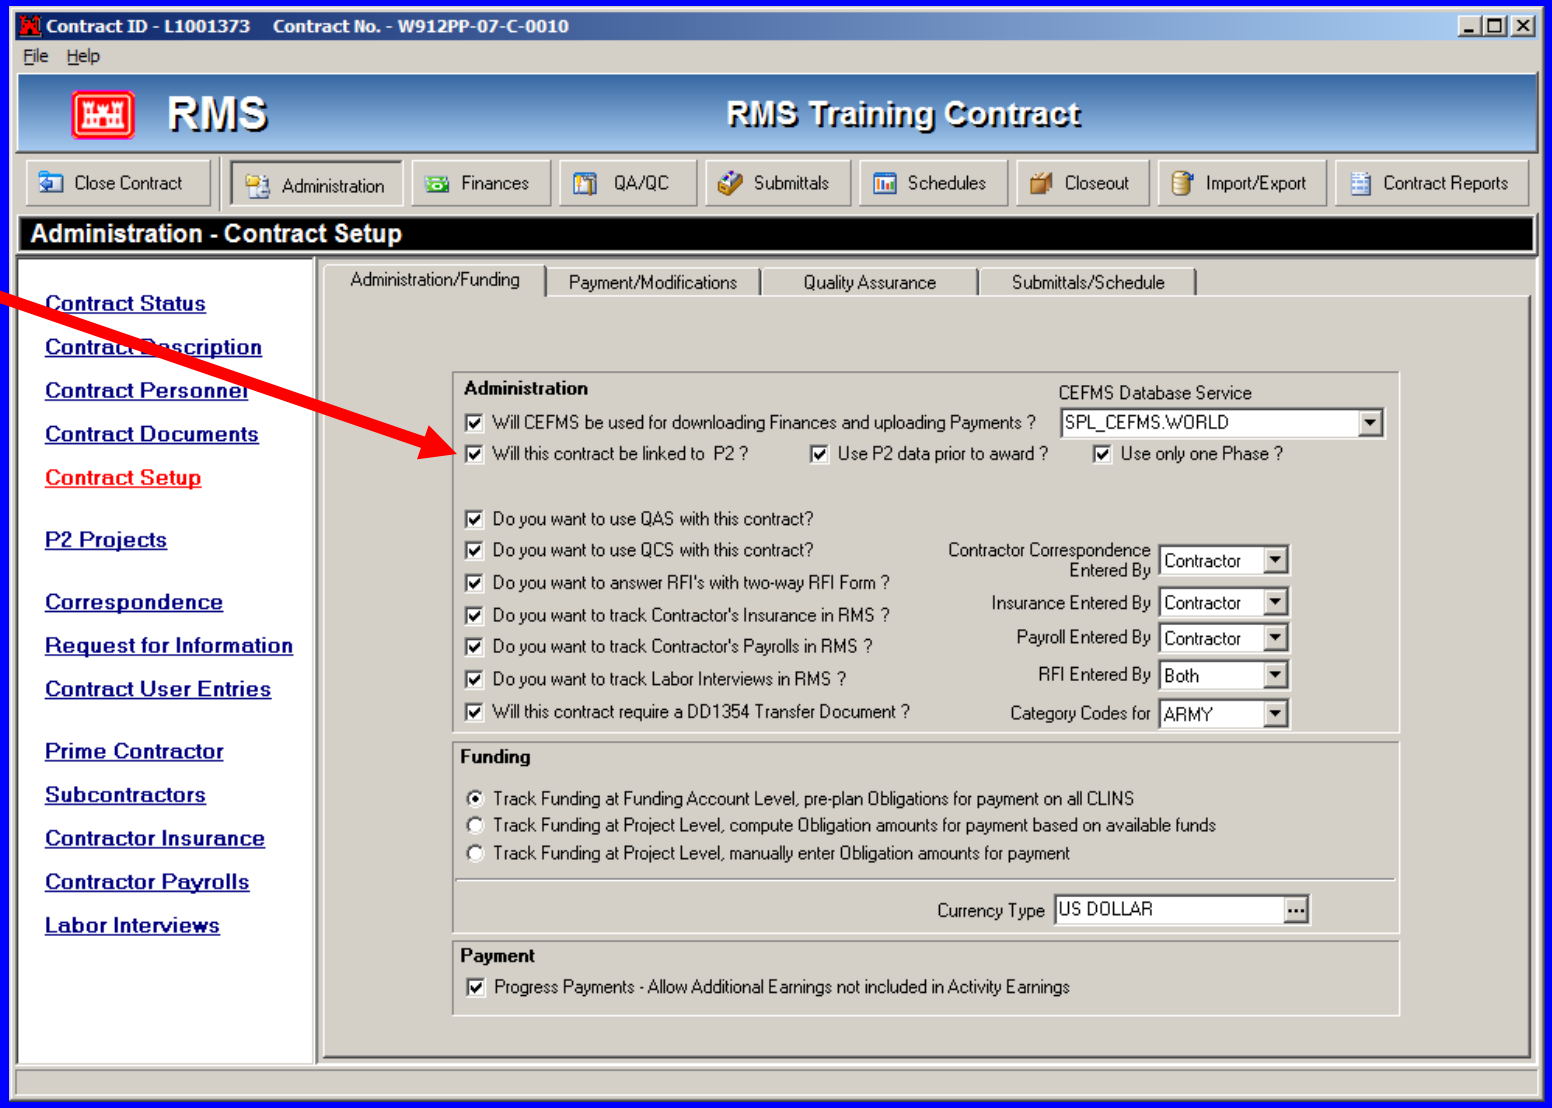

US Army Corps of Engineers ®

Multi-Phase Contracts in RMS

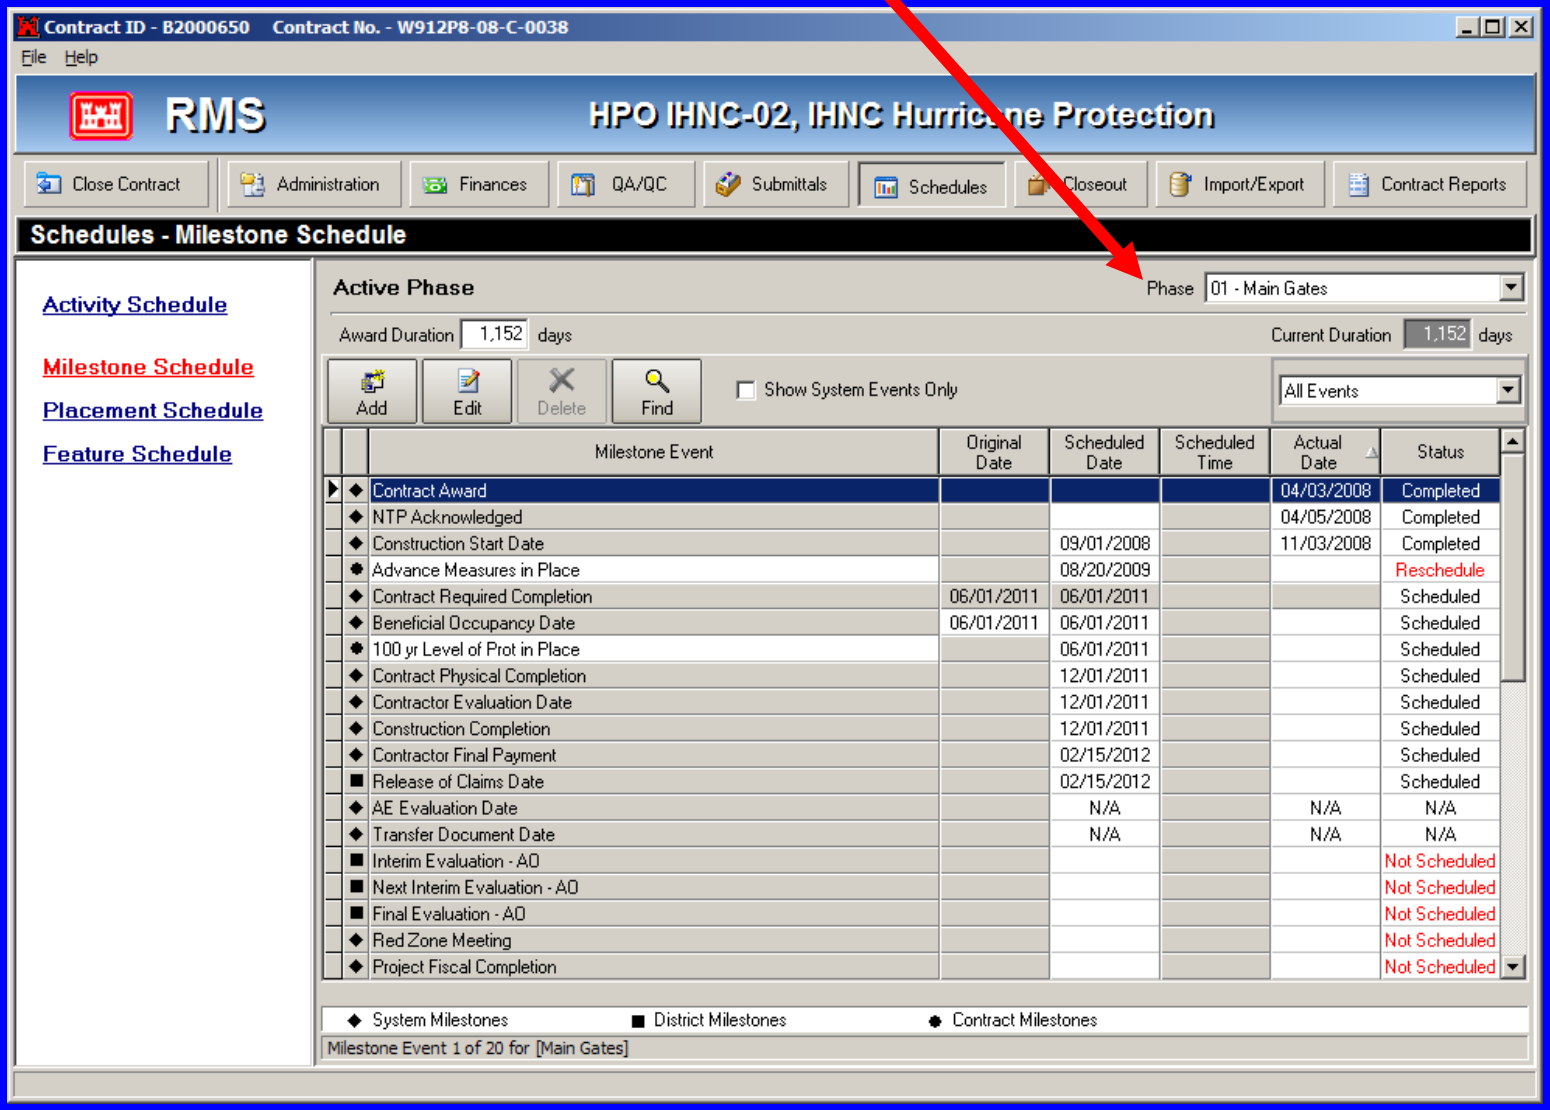
Contract ID - B2000650 Contract No. - W912P8-08-C-0038
File Help
RMS
HPO IHNC-02, IHNC Hurricane Protection
Close Contract
Administration
Finances
QA/QC
Submittals
Schedules
Closeout
Import/Export
Contract Reports
Schedules - Milestone Schedule
Activity Schedule
Milestone Schedule
Placement Schedule
Feature Schedule
Active Phase
Phase 01 - Main Gates
Award Duration 1,152 days
Current Duration 1,152 days
Add
Edit
Delete
Find
Show System Events Only
All Events
Milestone Event | Original Date | Scheduled Date | Scheduled Time | Actual Date | Status
Contract Award | | | | 04/03/2008 | Completed
NTP Acknowledged | | | | 04/05/2008 | Completed
Construction Start Date | | 09/01/2008 | | 11/03/2008 | Completed
Advance Measures in Place | | 08/20/2009 | | | Reschedule
Contract Required Completion | 06/01/2011 | 06/01/2011 | | | Scheduled
Beneficial Occupancy Date | 06/01/2011 | 06/01/2011 | | | Scheduled
100 yr Level of Prot in Place | | 06/01/2011 | | | Scheduled
Contract Physical Completion | | 12/01/2011 | | | Scheduled
Contractor Evaluation Date | | 12/01/2011 | | | Scheduled
Construction Completion | | 12/01/2011 | | | Scheduled
Contractor Final Payment | | 02/15/2012 | | | Scheduled
Release of Claims Date | | 02/15/2012 | | | Scheduled
AE Evaluation Date | | N/A | | N/A | N/A
Transfer Document Date | | N/A | | N/A | N/A
Interim Evaluation - AO | | | | | Not Scheduled
Next Interim Evaluation - AO | | | | | Not Scheduled
Final Evaluation - AO | | | | | Not Scheduled
Red Zone Meeting | | | | | Not Scheduled
Project Fiscal Completion | | | | | Not Scheduled
System Milestones
District Milestones
Contract Milestones
Milestone Event 1 of 20 for [Main Gates]

US Army Corps of Engineers ®

Information Interchanged from RMS to P2

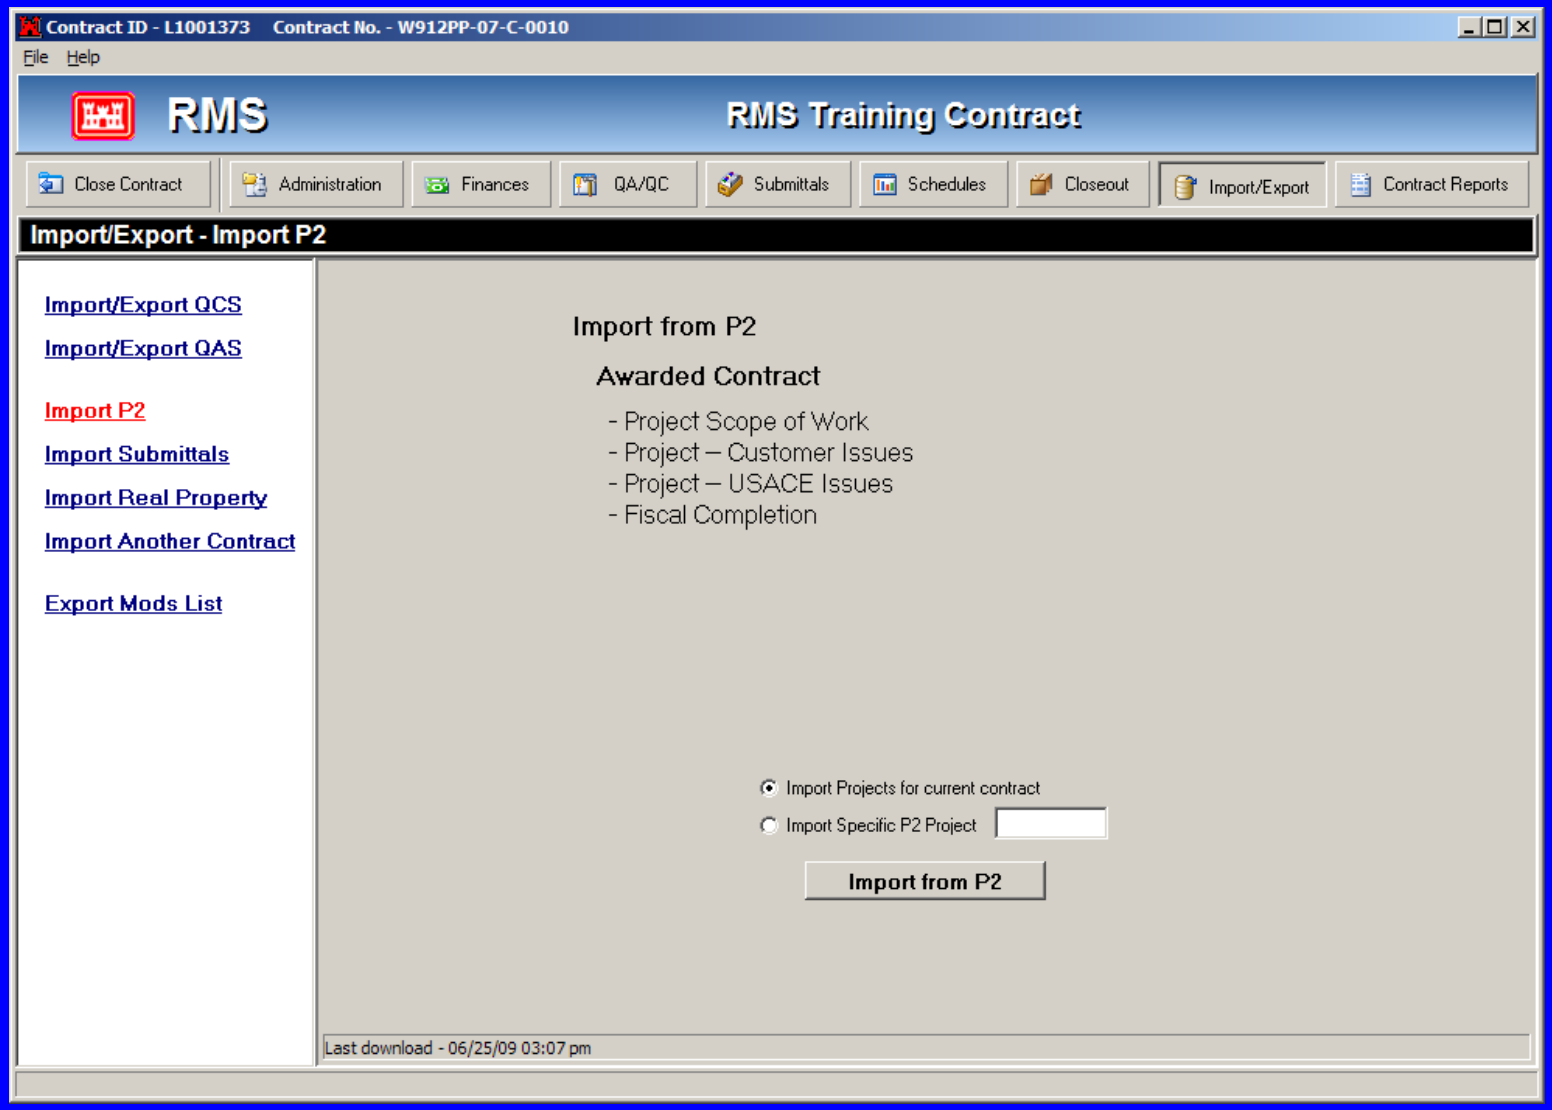

US Army Corps of Engineers ®

P2 – RMS Interface

- RMS defined dates are maintained via constraints in Primavera
- Manually entered overrides will be overwritten from RMS during the next update cycle
- Interface does NOT reschedule the project

US Army Corps of Engineers ®

P2 – RMS Interface

- You **MUST** use construction plug-ins

- To remove constraints
  - Remove the constraint
  - Reschedule the project
  - Remove the date from RMS
  - Reschedule project

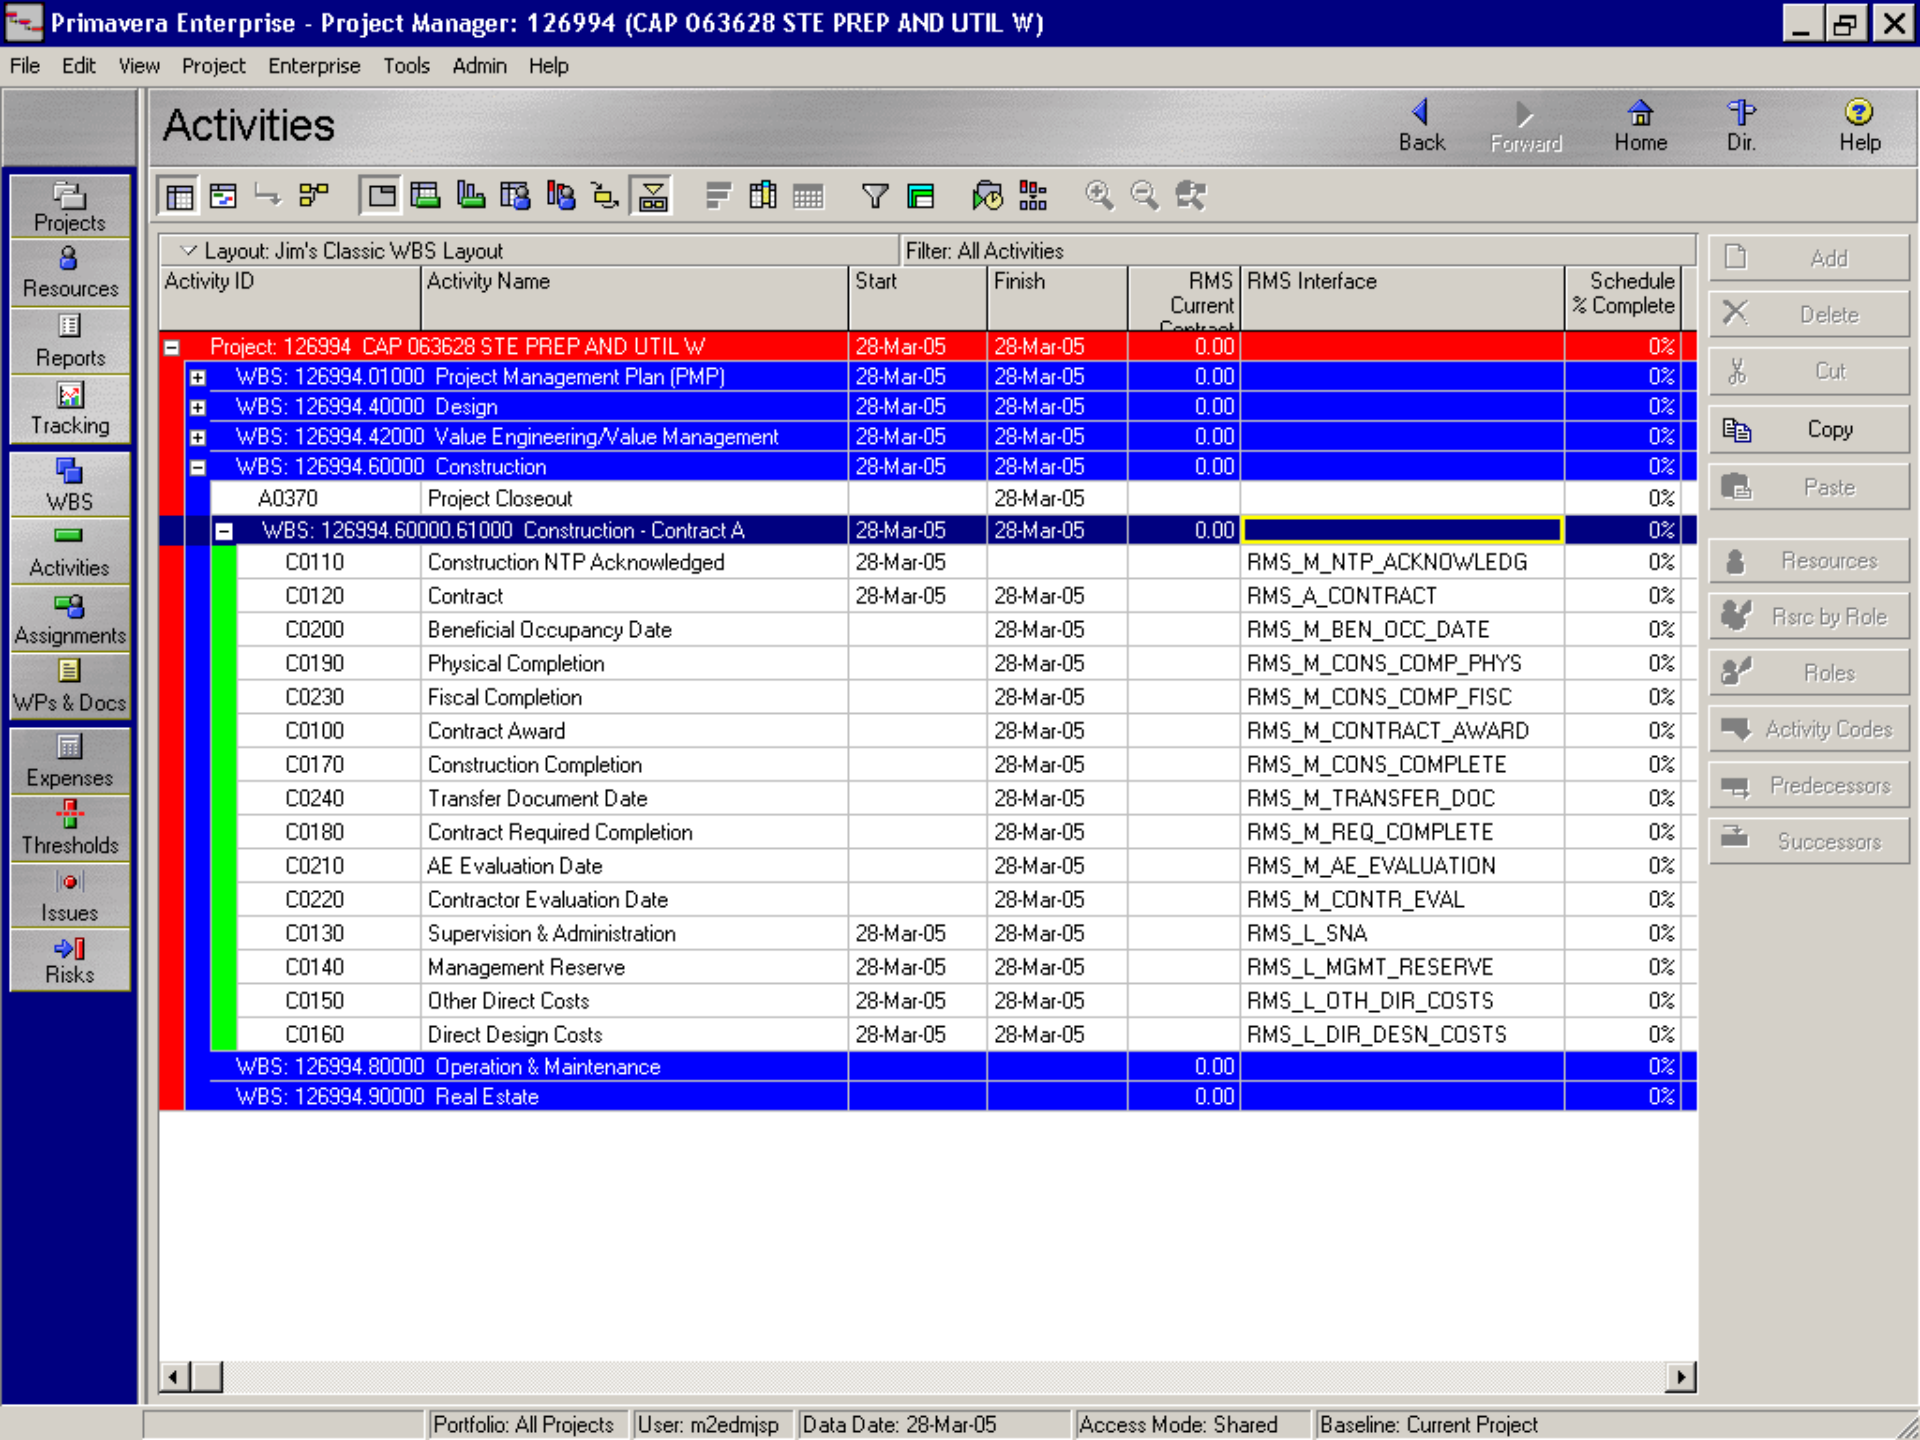
Primavera Enterprise - Project Manager: 126994 (CAP 063628 STE PREP AND UTIL W)
File Edit View Project Enterprise Tools Admin Help
Activities
Back Forward Home Dir. Help
Projects Resources Reports Tracking WBS Activities Assignments WPs & Docs Expenses Thresholds Issues Risks
Layout: Jim's Classic WBS Layout
Filter: All Activities
Activity ID | Activity Name | Start | Finish | RMS Current Contract | RMS Interface | Schedule % Complete
Project: 126994 CAP 063628 STE PREP AND UTIL W | 28-Mar-05 | 28-Mar-05 | 0.00 | | 0%
WBS: 126994.01000 Project Management Plan (PMP) | 28-Mar-05 | 28-Mar-05 | 0.00 | | 0%
WBS: 126994.40000 Design | 28-Mar-05 | 28-Mar-05 | 0.00 | | 0%
WBS: 126994.42000 Value Engineering/Value Management | 28-Mar-05 | 28-Mar-05 | 0.00 | | 0%
WBS: 126994.60000 Construction | 28-Mar-05 | 28-Mar-05 | 0.00 | | 0%
A0370 Project Closeout | | 28-Mar-05 | | | 0%
WBS: 126994.60000.61000 Construction - Contract A | 28-Mar-05 | 28-Mar-05 | 0.00 | | 0%
C0110 Construction NTP Acknowledged | 28-Mar-05 | | | RMS_M_NTP_ACKNOWLEDG | 0%
C0120 Contract | 28-Mar-05 | 28-Mar-05 | | RMS_A_CONTRACT | 0%
C0200 Beneficial Occupancy Date | | 28-Mar-05 | | RMS_M_BEN_OCC_DATE | 0%
C0190 Physical Completion | | 28-Mar-05 | | RMS_M_CONS_COMP_PHYS | 0%
C0230 Fiscal Completion | | 28-Mar-05 | | RMS_M_CONS_COMP_FISC | 0%
C0100 Contract Award | | 28-Mar-05 | | RMS_M_CONTRACT_AWARD | 0%
C0170 Construction Completion | | 28-Mar-05 | | RMS_M_CONS_COMPLETE | 0%
C0240 Transfer Document Date | | 28-Mar-05 | | RMS_M_TRANSFER_DOC | 0%
C0180 Contract Required Completion | | 28-Mar-05 | | RMS_M_REQ_COMPLETE | 0%
C0210 AE Evaluation Date | | 28-Mar-05 | | RMS_M_AE_EVALUATION | 0%
C0220 Contractor Evaluation Date | | 28-Mar-05 | | RMS_M_CONTR_EVAL | 0%
C0130 Supervision & Administration | 28-Mar-05 | 28-Mar-05 | | RMS_L_SNA | 0%
C0140 Management Reserve | 28-Mar-05 | 28-Mar-05 | | RMS_L_MGMT_RESERVE | 0%
C0150 Other Direct Costs | 28-Mar-05 | 28-Mar-05 | | RMS_L_OTH_DIR_COSTS | 0%
C0160 Direct Design Costs | 28-Mar-05 | 28-Mar-05 | | RMS_L_DIR_DESN_COSTS | 0%
WBS: 126994.80000 Operation & Maintenance | | | 0.00 | | 0%
WBS: 126994.90000 Real Estate | | | 0.00 | | 0%
Add Delete Cut Copy Paste Resources Rsrc by Role Roles Activity Codes Predecessors Successors
Portfolio: All Projects User: m2edmjsp Data Date: 28-Mar-05 Access Mode: Shared Baseline: Current Project

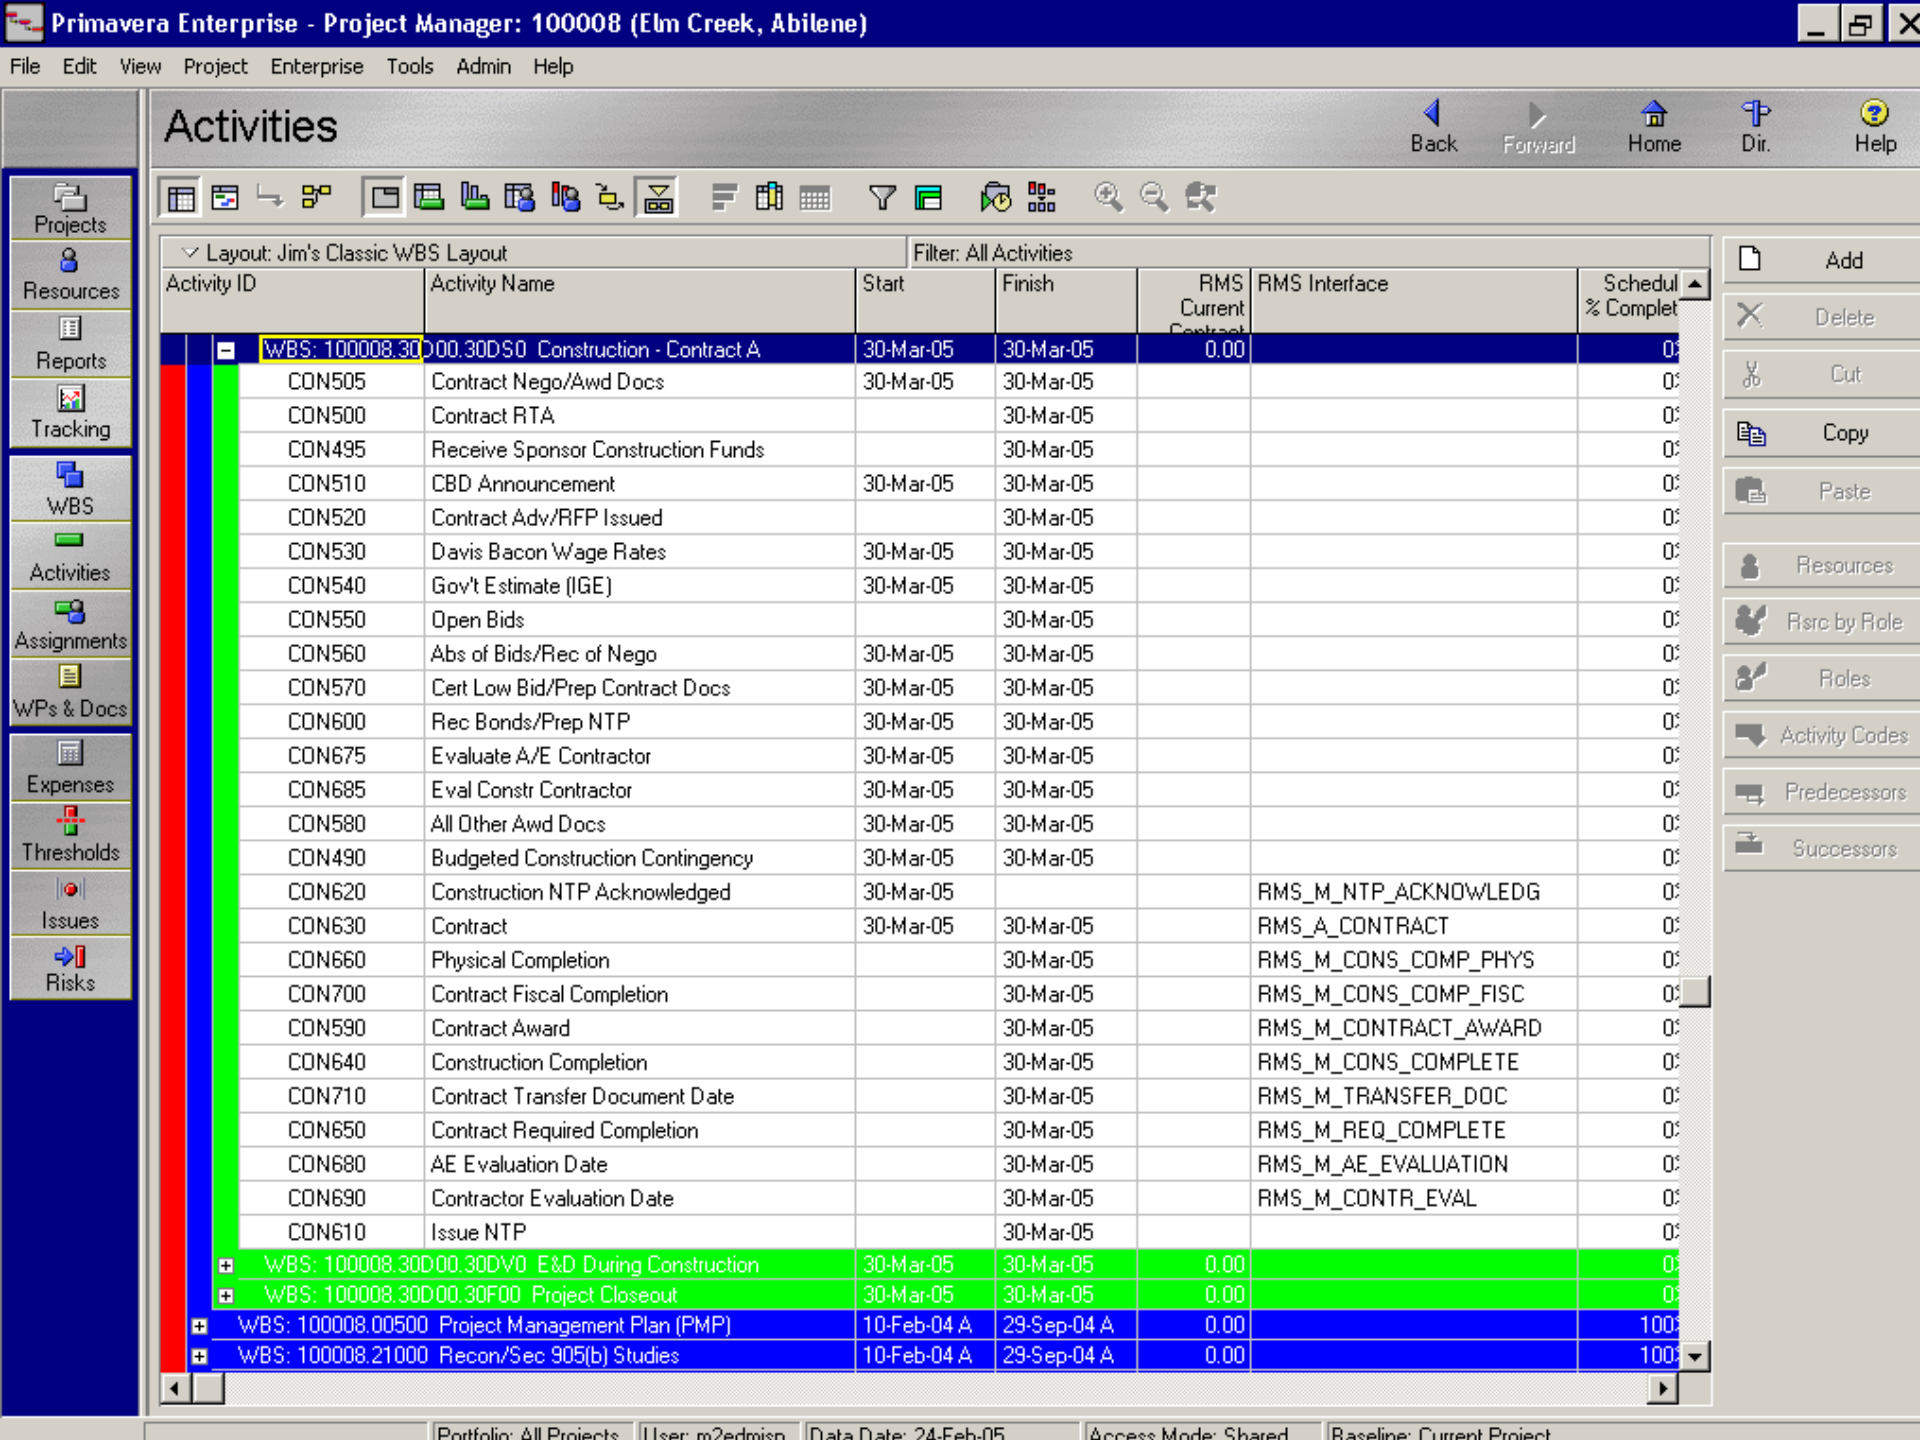
Primavera Enterprise - Project Manager: 100008 (Elm Creek, Abilene)
File Edit View Project Enterprise Tools Admin Help
Activities
Back Forward Home Dir. Help
Projects Resources Reports Tracking WBS Activities Assignments WPs & Docs Expenses Thresholds Issues Risks
Layout: Jim's Classic WBS Layout
Filter: All Activities
Activity ID | Activity Name | Start | Finish | RMS Current Contract | RMS Interface | Schedul % Complet
WBS: 100008.30D00.30DS0 Construction - Contract A | 30-Mar-05 | 30-Mar-05 | 0.00
CON505 Contract Nego/Awd Docs | 30-Mar-05 | 30-Mar-05
CON500 Contract RTA | 30-Mar-05
CON495 Receive Sponsor Construction Funds | 30-Mar-05
CON510 CBD Announcement | 30-Mar-05 | 30-Mar-05
CON520 Contract Adv/RFP Issued | 30-Mar-05
CON530 Davis Bacon Wage Rates | 30-Mar-05 | 30-Mar-05
CON540 Gov't Estimate (IGE) | 30-Mar-05 | 30-Mar-05
CON550 Open Bids | 30-Mar-05
CON560 Abs of Bids/Rec of Nego | 30-Mar-05 | 30-Mar-05
CON570 Cert Low Bid/Prep Contract Docs | 30-Mar-05 | 30-Mar-05
CON600 Rec Bonds/Prep NTP | 30-Mar-05 | 30-Mar-05
CON675 Evaluate A/E Contractor | 30-Mar-05 | 30-Mar-05
CON685 Eval Constr Contractor | 30-Mar-05 | 30-Mar-05
CON580 All Other Awd Docs | 30-Mar-05 | 30-Mar-05
CON490 Budgeted Construction Contingency | 30-Mar-05 | 30-Mar-05
CON620 Construction NTP Acknowledged | 30-Mar-05 | RMS_M_NTP_ACKNOWLEDG
CON630 Contract | 30-Mar-05 | 30-Mar-05 | RMS_A_CONTRACT
CON660 Physical Completion | 30-Mar-05 | RMS_M_CONS_COMP_PHYS
CON700 Contract Fiscal Completion | 30-Mar-05 | RMS_M_CONS_COMP_FISC
CON590 Contract Award | 30-Mar-05 | RMS_M_CONTRACT_AWARD
CON640 Construction Completion | 30-Mar-05 | RMS_M_CONS_COMPLETE
CON710 Contract Transfer Document Date | 30-Mar-05 | RMS_M_TRANSFER_DOC
CON650 Contract Required Completion | 30-Mar-05 | RMS_M_REQ_COMPLETE
CON680 AE Evaluation Date | 30-Mar-05 | RMS_M_AE_EVALUATION
CON690 Contractor Evaluation Date | 30-Mar-05 | RMS_M_CONTR_EVAL
CON610 Issue NTP | 30-Mar-05
WBS: 100008.30D00.30DV0 E&D During Construction | 30-Mar-05 | 30-Mar-05 | 0.00
WBS: 100008.30D00.30F00 Project Closeout | 30-Mar-05 | 30-Mar-05 | 0.00
WBS: 100008.00500 Project Management Plan (PMP) | 10-Feb-04 A | 29-Sep-04 A | 0.00 | 100
WBS: 100008.21000 Recon/Sec 905(b) Studies | 10-Feb-04 A | 29-Sep-04 A | 0.00 | 100
Add Delete Cut Copy Paste Resources Rsrc by Role Roles Activity Codes Predecessors Successors
Portfolio: All Projects User: m2edmisp Data Date: 24-Feb-05 Access Mode: Shared Baseline: Current Project

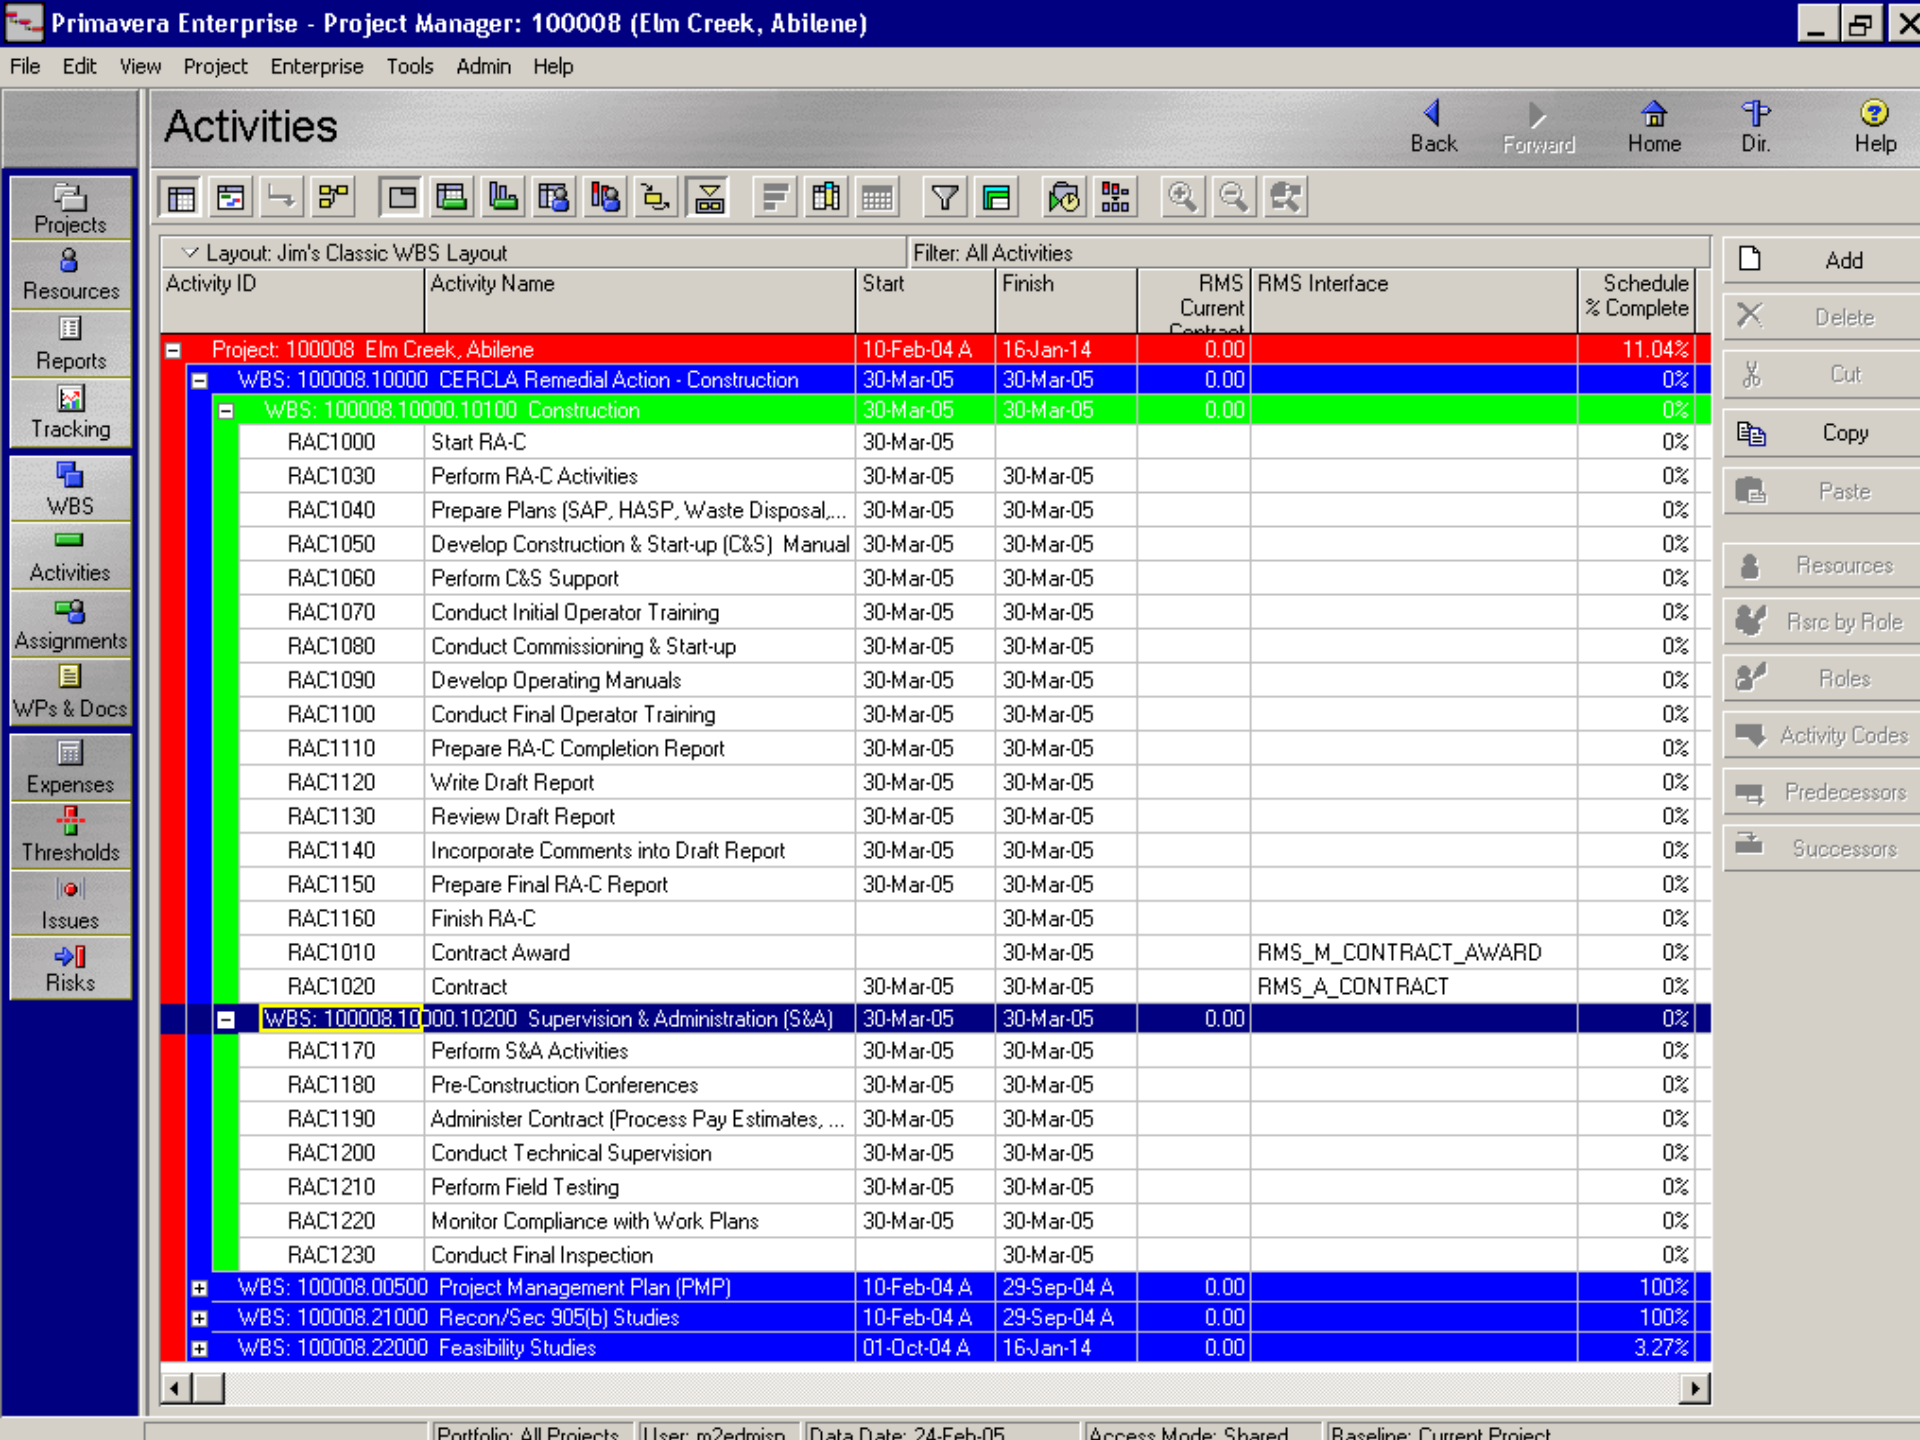
Primavera Enterprise - Project Manager: 100008 (Elm Creek, Abilene)
File Edit View Project Enterprise Tools Admin Help
Activities
Back Forward Home Dir. Help
Projects Resources Reports Tracking WBS Activities Assignments WPs & Docs Expenses Thresholds Issues Risks
Layout: Jim's Classic WBS Layout
Filter: All Activities
Activity ID | Activity Name | Start | Finish | RMS Current Contract | RMS Interface | Schedule % Complete
Project: 100008 Elm Creek, Abilene | 10-Feb-04 A | 16-Jan-14 | 0.00 | | 11.04%
WBS: 100008.10000 CERCLA Remedial Action - Construction | 30-Mar-05 | 30-Mar-05 | 0.00 | | 0%
WBS: 100008.10000.10100 Construction | 30-Mar-05 | 30-Mar-05 | 0.00 | | 0%
RAC1000 Start RA-C | 30-Mar-05 | | | | 0%
RAC1030 Perform RA-C Activities | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1040 Prepare Plans (SAP, HASP, Waste Disposal,... | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1050 Develop Construction & Start-up (C&S) Manual | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1060 Perform C&S Support | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1070 Conduct Initial Operator Training | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1080 Conduct Commissioning & Start-up | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1090 Develop Operating Manuals | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1100 Conduct Final Operator Training | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1110 Prepare RA-C Completion Report | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1120 Write Draft Report | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1130 Review Draft Report | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1140 Incorporate Comments into Draft Report | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1150 Prepare Final RA-C Report | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1160 Finish RA-C | | 30-Mar-05 | | | 0%
RAC1010 Contract Award | | 30-Mar-05 | | RMS_M_CONTRACT_AWARD | 0%
RAC1020 Contract | 30-Mar-05 | 30-Mar-05 | | RMS_A_CONTRACT | 0%
WBS: 100008.10000.10200 Supervision & Administration (S&A) | 30-Mar-05 | 30-Mar-05 | 0.00 | | 0%
RAC1170 Perform S&A Activities | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1180 Pre-Construction Conferences | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1190 Administer Contract (Process Pay Estimates, ... | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1200 Conduct Technical Supervision | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1210 Perform Field Testing | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1220 Monitor Compliance with Work Plans | 30-Mar-05 | 30-Mar-05 | | | 0%
RAC1230 Conduct Final Inspection | | 30-Mar-05 | | | 0%
WBS: 100008.00500 Project Management Plan (PMP) | 10-Feb-04 A | 29-Sep-04 A | 0.00 | | 100%
WBS: 100008.21000 Recon/Sec 905(b) Studies | 10-Feb-04 A | 29-Sep-04 A | 0.00 | | 100%
WBS: 100008.22000 Feasibility Studies | 01-Oct-04 A | 16-Jan-14 | 0.00 | | 3.27%
Add Delete Cut Copy Paste Resources Rsrc by Role Roles Activity Codes Predecessors Successors
Portfolio: All Projects User: m2edmisp Data Date: 24-Feb-05 Access Mode: Shared Baseline: Current Project

Adobe Acrobat Professional - [USACE RMS - P2 Linking Status.pdf]
File Edit View Document Comments Tools Advanced Window Help
Search Create PDF Comment & Markup Send for Review Secure Sign Forms
Select 95% Help

District / Division	Construction Contracts in RMS and P2					P2 Projects Linked to RMS Contracts			
	Total Number of Construction Contracts in RMS	Total Number of Construction Contracts in P2	Percent Of Contracts In P2	Number of Construction Contracts Not in P2	Percent of Contracts not in P2	Number of Construction Contracts In P2 Linked to RMS	Percent of Contracts in P2 Linked to RMS	Number of Contracts in P2 Not Linked to RMS	Percent of Contracts in P2 Not Linked to RMS
MVD (continued)									
MVN	126	141	112%	0	0%	23	16%	118	84%
MVM	53	73	138%	0	0%	20	27%	53	73%
MVK	168	87	52%	81	48%	44	51%	43	49%
MVR	34	11	32%	23	68%	11	100%	0	0%
Total for MVD	482	394	82%	123	18%	134	34%	260	66%
TAC									
TAC	456	174	38%	282	62%	120	69%	54	31%
Total for TAC	456	174	38%	282	62%	120	69%	54	31%
SWD									
SWT	345	161	47%	184	53%	120	75%	41	25%
SWG	213	63	30%	150	70%	61	97%	2	3%
SWF	519	399	77%	120	23%	334	84%	65	16%
SWL	136	33	24%	103	76%	28	85%	5	15%
Total for SWD	1,213	656	54%	557	46%	543	83%	113	17%
NWD									
NWK	212	86	41%	126	59%	41	48%	45	52%
NWP	53	22	42%	31	58%	21	95%	1	5%
NWS	439	160	36%	279	64%	101	63%	59	37%
NWW	58	17	29%	41	71%	17	100%	0	0%
NWO	318	100	31%	218	69%	64	64%	36	36%
Total for NWD	1,080	385	36%	695	64%	244	63%	141	37%
SPD									
SPN	39	0	0%	39	100%	0	0%	0	0%
SPK	203	68	33%	135	67%	32	47%	36	53%
SPA	95	34	36%	61	64%	23	68%	11	32%
SPL	602	230	38%	372	62%	161	70%	69	30%
Total for SPD	939	332	35%	607	65%	216	65%	116	35%
POD									
POF	348	227	65%	121	35%	153	67%	74	33%
POH	301	165	55%	136	45%	157	95%	8	5%
POJ	155	153	99%	2	1%	152	99%	1	1%
POA	186	128	69%	58	31%	108	84%	20	16%

Bookmarks Signatures Pages Attachments Comments
11.00 x 8.50 in
2 of 3

US Army Corps of Engineers ®

P2 – RMS Interface

Questions?
